


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04							
							S	M	T	W	T			
1	<b>Contract Signed</b>	0 days	Mon 4/12/04	Mon 4/12/04		Boulder County and Hart								
2	<b>Kickoff Meeting with Customer</b>	1 hr	Mon 4/12/04	Mon 4/12/04	1	Boulder County and Hart								
3	<b>Order Hardware</b>	1 day	Mon 4/12/04	Mon 4/12/04										
4	eSlate Components	0.5 days	Mon 4/12/04	Mon 4/12/04		Hart Technical Support								
5	Application Hardware and Peripherals	0.5 days	Mon 4/12/04	Mon 4/12/04	4	Hart Technical Support								
6	<b>Order Software</b>	1 day	Mon 4/12/04	Tue 4/13/04										
7	eSlate Software	0.5 days	Mon 4/12/04	Mon 4/12/04	4	Hart Technical Support								
8	3rd Party Software	0.5 days	Tue 4/13/04	Tue 4/13/04	7	Hart Technical Support								
9	<b>Work Process Analysis</b>	18 days	Tue 4/13/04	Wed 5/5/04										
10	Initial Data Collection	4 days	Tue 4/13/04	Fri 4/16/04		Hart PM and BC Staff								
11	Workflow Analysis	4.88 days	Mon 4/19/04	Fri 4/23/04	10	Hart PM								
12	Reports Requirements Analysis	1 day	Mon 4/26/04	Mon 4/26/04	11	Hart PM and BC Staff								
13	Variance Analysis	1 day	Tue 4/27/04	Tue 4/27/04	12	Hart PM								
14	Update and Refine Project Plan	1 day	Wed 4/28/04	Wed 4/28/04	13	Hart PM and BC Staff								
15	Write Report	3 days	Thu 4/29/04	Mon 5/3/04	14	Hart PM								
16	Customer Review and Accept Report and Project Plan	2 days	Tue 5/4/04	Wed 5/5/04	15	BC Project Team								
17	<b>Implementation Project Team Meetings</b>	192.13 days	Fri 4/16/04	Thu 12/16/04										
18	Weekly Project Team Meetings	172 days	Fri 4/16/04	Mon 12/13/04	2	Boulder County and Hart								
19	Monthly Project Review Meetings	149.5 days	Fri 5/21/04	Thu 12/16/04	2FS+30 days	Boulder County and Hart								
20	<b>Community Outreach</b>	67 days	Mon 4/12/04	Mon 7/12/04	2									
21	VEO Campaign Team Meetings per Contract	65 days	Mon 4/12/04	Mon 7/12/04	2	Hart VEO Support and BC								
22	Develop Voter Outreach and Education Campaign Plan	7 days	Mon 4/12/04	Wed 4/21/04		Hart VEO Support and BC								
23	Create VEO Materials	13 days	Wed 4/21/04	Mon 5/10/04	22	Hart VEO Support								
24	<b>Custom Engineering Projects</b>	72.13 days	Mon 4/19/04	Fri 7/23/04										
25	Develop Project Requirements	15 days	Mon 4/19/04	Fri 5/7/04		Hart Development Team								
26	Customer Review and Approve Requirements	2 days	Mon 5/10/04	Tue 5/11/04	25	BC Project Team								
27	Develop Specific Project Plans	3 days	Wed 5/12/04	Fri 5/14/04	26	Hart Development Suppo								
28	Engineering Development and Testing	53 days	Wed 5/12/04	Fri 7/23/04		Hart Development Suppo								
29	Deliver Envelope and Signature Scan	1 day	Mon 7/12/04	Mon 7/12/04	26FS+10 day	Hart Development Suppo								



Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04				
								S	M	T	W	T
30		Deliver Automated Ballot Now	1 day	Mon 7/19/04	Mon 7/19/04		Hart Development Suppo					
31		Deliver Custom Reports	1 day	Fri 7/23/04	Fri 7/23/04	30	Hart Development Suppo					
32		<b>Develop Training Plan</b>	<b>5 days</b>	<b>Mon 4/26/04</b>	<b>Fri 4/30/04</b>							
33		Create Customized Training Plan	3 days	Mon 4/26/04	Wed 4/28/04	10	Hart Training Support					
34		Customer Review and Accept Training Plan	2 days	Thu 4/29/04	Fri 4/30/04	33	BC Project Team					
35		<b>Warehouse Facilities and Operations</b>	<b>30 days</b>	<b>Mon 4/26/04</b>	<b>Fri 6/4/04</b>							
36		Develop Warehouse Operations Plan	5 days	Mon 4/26/04	Fri 4/30/04	11	Boulder County and Hart					
37		Prepare Warehouse for Ballot Now Election Operations	25 days	Mon 5/3/04	Fri 6/4/04	36	BC Project Team					
38		<b>Configure and Deploy Application Hardware</b>	<b>15 days</b>	<b>Mon 5/10/04</b>	<b>Fri 5/28/04</b>							
39		Receive Hardware at Hart Office	0.5 days	Mon 5/10/04	Mon 5/10/04	5FS+20 days	Hart Technical Support					
40		Configure eSlate Applications and Test Hardware	10 days	Fri 5/14/04	Thu 5/27/04	39	Hart Technical Support					
41		Ship Hardware	1 day	Fri 5/28/04	Fri 5/28/04	40	Hart Technical Support					
42		<b>Deliver Application and Training Hardware</b>	<b>6 days</b>	<b>Fri 5/21/04</b>	<b>Fri 5/28/04</b>							
43		eSlate Training Hardware Delivered	0.5 days	Fri 5/21/04	Fri 5/21/04							
44		eSlate Application Hardware Received by Customer	0.2 days	Fri 5/28/04	Fri 5/28/04		BC Project Team					
45		eSlate Application Hardware Setup and Test	0.8 days	Fri 5/28/04	Fri 5/28/04	44	Hart Trainer Support					
46		<b>Customer Staff Training</b>	<b>5 days</b>	<b>Mon 5/24/04</b>	<b>Fri 5/28/04</b>							
47		Administrative Overview	2 hrs	Mon 5/24/04	Mon 5/24/04		Hart Training Support anc					
48		Ballot Now Polling Place Operations	4 hrs	Mon 5/24/04	Mon 5/24/04	47	Hart Training Support anc					
49		BOSS	1 day	Mon 5/24/04	Tue 5/25/04	48	Hart Training Support anc					
50		Ballot Now	2 days	Tue 5/25/04	Thu 5/27/04	49	Hart Training Support anc					
51		Tally/Rally	6 hrs	Thu 5/27/04	Fri 5/28/04	50	Hart Training Support anc					
52		Rally Substation Operator	2 hrs	Fri 5/28/04	Fri 5/28/04	51	Hart Training Support anc					
53		Logic and Accuracy Testing	2 hrs	Fri 5/28/04	Fri 5/28/04	52	Hart Training Support anc					
54		<b>Acceptance Testing</b>	<b>1.97 days</b>	<b>Tue 6/1/04</b>	<b>Wed 6/2/04</b>	<b>53</b>						
55		Create BOSS Database	2 hrs	Tue 6/1/04	Tue 6/1/04		Hart PM and BC Staff					
56		Proof Ballot Content	0.5 hrs	Tue 6/1/04	Tue 6/1/04	55	Hart PM and BC Staff					
57		Create MBBs	0.5 hrs	Tue 6/1/04	Tue 6/1/04	56	Hart PM and BC Staff					
58		Print Ballots on all workstations	5 hrs	Tue 6/1/04	Tue 6/1/04	57	Hart PM and BC Staff					

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04				
								S	M	T	W	T
59		Vote ED, AV, Early Ballots	1 hr	Wed 6/2/04	Wed 6/2/04	58	Hart PM and BC Staff					
60		Scan and Resolve Ballots on all Workstations specifying AV, EV, E	4 hrs	Wed 6/2/04	Wed 6/2/04	59	Hart PM and BC Staff					
61		Read MBBs from AV, EV and ED into Tally	0.5 hrs	Wed 6/2/04	Wed 6/2/04	60	Hart PM and BC Staff					
62		Read MBBs from ED Remote Counting Station (RCS) into Rally	0.5 hrs	Wed 6/2/04	Wed 6/2/04	61						
63		Tabulate Results and Generate Reports	1 hr	Wed 6/2/04	Wed 6/2/04	62	Hart PM and BC Staff					
64		Validate Report Data	0.5 hrs	Wed 6/2/04	Wed 6/2/04	63	Hart PM and BC Staff					
65		Customer Acceptance (except custom engineering projects)	0.25 hrs	Wed 6/2/04	Wed 6/2/04	64	Hart PM and BC Staff					
66		<b>Payment Milestone One</b>	1 day	Wed 6/2/04	Thu 6/3/04	65						
67		<b>Workflow and Resource Planning</b>	<b>1.32 days</b>	<b>Thu 6/10/04</b>	<b>Fri 6/11/04</b>							
96		<b>Mock Election (End-To-End System Test)</b>	<b>31.13 days</b>	<b>Mon 6/14/04</b>	<b>Fri 7/23/04</b>							
97		Create Mock Election Plan	1 day	Mon 6/14/04	Mon 6/14/04		Boulder County and Hart					
98		Create BOSS Database	0.5 hrs	Fri 6/18/04	Fri 6/18/04	97	Boulder County and Hart					
99		Proof Ballot Content	0.5 hrs	Fri 6/18/04	Fri 6/18/04	98	Boulder County and Hart					
100		Setup Mock Polling Place Equipment EV	0.5 hrs	Thu 7/22/04	Thu 7/22/04	99	Boulder County and Hart					
101		Setup Mock Polling Place Equipment ED	0.5 hrs	Thu 7/22/04	Thu 7/22/04	100	Boulder County and Hart					
102		Setup Central Count Station	3 hrs	Thu 7/22/04	Thu 7/22/04	101	Boulder County and Hart					
103		Create MBBs	0.25 hrs	Fri 7/23/04	Fri 7/23/04	102	Boulder County and Hart					
104		Print AV Ballots	0.5 hrs	Fri 7/23/04	Fri 7/23/04	103	Boulder County and Hart					
105		Print ED Ballots	0.5 hrs	Fri 7/23/04	Fri 7/23/04	104	Boulder County and Hart					
106		Print EV Ballots with Automated Ballot Now ballot on demand	0.5 hrs	Fri 7/23/04	Fri 7/23/04	105	Boulder County and Hart					
107		Vote EV Ballots	0.5 hrs	Fri 7/23/04	Fri 7/23/04	106	Boulder County and Hart					
108		Vote AV Ballots	0.5 hrs	Fri 7/23/04	Fri 7/23/04	107	Boulder County and Hart					
109		Vote ED Ballots	0.5 hrs	Fri 7/23/04	Fri 7/23/04	108	Boulder County and Hart					
110		Envelope Scan and Signature Capture and Compare Process	0.5 hrs	Fri 7/23/04	Fri 7/23/04	109	Boulder County and Hart					
111		Central Count Station Operations	0.25 hrs	Fri 7/23/04	Fri 7/23/04	110	Boulder County and Hart					
112		Scan and Resolve AV, EV and ED Ballots using all workstations	1.25 hrs	Fri 7/23/04	Fri 7/23/04	111	Boulder County and Hart					
113		Read MBBs from AV, EV and ED into Tally	0.5 hrs	Fri 7/23/04	Fri 7/23/04	112	Boulder County and Hart					
114		Read MBBs from ED Remote Counting Station (RCS) into Rally	0.25 hrs	Fri 7/23/04	Fri 7/23/04	113	Boulder County and Hart					
115		Tabulate Results and Generate Reports	0.5 hrs	Fri 7/23/04	Fri 7/23/04	114	Boulder County and Hart					

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04				
								S	M	T	W	T
116		Generate Custom Fusion Reports	0.5 hrs	Fri 7/23/04	Fri 7/23/04	115	Boulder County and Hart					
117		Conduct Mock Election Review	1 hr	Fri 7/23/04	Fri 7/23/04	116	Boulder County and Hart					
118		<b>Payment Milestone Two</b>	0 days	Fri 7/23/04	Fri 7/23/04	117	Boulder County and Hart					
119		<b>August 10, 2004 Primary Election</b>	<b>61.5 days</b>	<b>Mon 6/14/04</b>	<b>Sun 8/22/04</b>							
120		<b>Pre-Election Preparation</b>	<b>5.5 days</b>	<b>Mon 6/14/04</b>	<b>Mon 6/21/04</b>							
121		Early Voting In-Person Site layout	1 day	Mon 6/14/04	Mon 6/14/04	90						
122		Election Day Site Preparation	4 days	Tue 6/15/04	Fri 6/18/04							
123		Ballot Language Certified by SOS	0 days	Tue 6/15/04	Tue 6/15/04							
124		Create BOSS Database	2 days	Tue 6/15/04	Wed 6/16/04	123						
125		Proof Ballot Content	3 hrs	Thu 6/17/04	Thu 6/17/04	124						
126		Create MBBs	3 hrs	Thu 6/17/04	Thu 6/17/04	125						
127		Round Trip Ballot Now	4 hrs	Thu 6/17/04	Fri 6/18/04	126						
128		Pre-Election L&A Tests-Ballot Now	2 hrs	Fri 6/18/04	Fri 6/18/04	127						
129		Create ballot quantities spreadsheet for Provisional, Absentee	8 hrs	Fri 6/18/04	Mon 6/21/04	128						
130		<b>Absentee Voting (AV) By-Mail</b>	<b>45.75 days</b>	<b>Thu 6/17/04</b>	<b>Tue 8/10/04</b>							
131		Create Ballot Now Ballot Print Files	5 hrs	Thu 6/17/04	Fri 6/18/04	126						
132		Print Absentee Ballots	14 days	Fri 6/18/04	Fri 7/9/04	131						
133		Mail Ballots	26 days	Wed 7/7/04	Tue 8/3/04	132SF						
134		Receive Voted Ballots	30 days	Sat 7/10/04	Tue 8/10/04	133SS						
135		AV Ballot Processing, Scanning and Resolution	11 days	Sat 7/31/04	Tue 8/10/04							
136		Write AV Results to MBB	0.5 hrs	Tue 8/10/04	Tue 8/10/04							
137		<b>Ballot Now Provisional Ballot Voting</b>	<b>40.5 days</b>	<b>Mon 7/12/04</b>	<b>Sun 8/22/04</b>							
138		Create Provisional Ballot Now Ballot Print Files	1 day	Mon 7/12/04	Mon 7/12/04							
139		Print Provisional Ballots	4 days	Tue 7/13/04	Fri 7/16/04	138						
140		Package Provisional Ballots and add to Election Day Precinct s	5 days	Mon 7/19/04	Fri 7/23/04							
141		Provisional Ballot Processing, Scanning and Resolution	12 days	Wed 8/11/04	Sun 8/22/04							
142		Write Provisional Results to MBB	0.5 hrs	Sun 8/22/04	Sun 8/22/04							
143		<b>Conduct Election Worker Training</b>	<b>9 days</b>	<b>Fri 7/30/04</b>	<b>Sat 8/7/04</b>							
144		Early Voting In-Person Poll Officials and Workers	1 day	Fri 7/30/04	Fri 7/30/04							

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04							
								S	M	T	W	T			
145		Election Day Poll Officials and Workers (County Conducts)	6 days	Mon 8/2/04	Sat 8/7/04										
146		Central Counting Staff	3 hrs	Sat 8/7/04	Sat 8/7/04	154									
147		Remote Counting Staff	3 hrs	Sat 8/7/04	Sat 8/7/04										
148		AV Ballot Processing and Resolution Team	2 hrs	Sat 7/31/04	Sat 7/31/04										
149		<b>Early Voting In-Person (EV)</b>	<b>11.06 days</b>	<b>Fri 7/30/04</b>	<b>Tue 8/10/04</b>										
150		Marshall Equipment for EV Locations	0.5 days	Fri 7/30/04	Fri 7/30/04										
151		Deploy Equipment to EV polling places	0.5 days	Fri 7/30/04	Fri 7/30/04										
152		Setup Polls	1 hr	Fri 7/30/04	Fri 7/30/04										
153		Disburse Supplies	1 day	Fri 7/30/04	Fri 7/30/04										
154		Conduct Early Voting	7 days	Sat 7/31/04	Fri 8/6/04										
155		Secure Polls	0.5 hrs	Sat 8/7/04	Sat 8/7/04										
156		Secure Ballot Cans at Central Count Station	1 hr	Sat 8/7/04	Sat 8/7/04										
157		Return Equipment to Warehouse	1 hr	Sat 8/7/04	Sat 8/7/04	154									
158		EV Ballot Processing, Scanning and Resolution	3 days	Sat 8/7/04	Tue 8/10/04	155									
159		<b>Election Day (ED) Voting</b>	<b>23 days</b>	<b>Mon 7/19/04</b>	<b>Tue 8/10/04</b>										
160		Marshal ED Equipment	12 days	Mon 7/19/04	Fri 7/30/04										
161		Deploy Equipment to ED polling places	5 days	Thu 8/5/04	Mon 8/9/04										
162		Disburse Supplies	3 days	Sat 8/7/04	Mon 8/9/04										
163		Setup Polls	0.5 hrs	Tue 8/10/04	Tue 8/10/04	164FF									
164		Conduct ED Voting	1 day	Tue 8/10/04	Tue 8/10/04										
165		Close Polls	0.5 hrs	Tue 8/10/04	Tue 8/10/04										
166		Secure Polls	0.3 hrs	Tue 8/10/04	Tue 8/10/04										
167		Receive voted ballots at Central Count Station	4 hrs	Tue 8/10/04	Tue 8/10/04										
168		Process voted ballots at Rally Station	1 hr	Tue 8/10/04	Tue 8/10/04										
169		<b>Central Counting Station Operations</b>	<b>23 days</b>	<b>Sat 7/31/04</b>	<b>Sun 8/22/04</b>										
170		Set-Up Central Count Station and Rally Station	4 hrs	Sat 7/31/04	Sat 7/31/04	135SS									
171		Practice Central Count Station Procedures including Rally	2 hrs	Sat 7/31/04	Sat 7/31/04	170									
172		<b>Tabulate Election Results</b>	<b>13 days</b>	<b>Tue 8/10/04</b>	<b>Sun 8/22/04</b>	<b>154</b>									
173		AV MBBs to Tally	0.2 hrs	Tue 8/10/04	Tue 8/10/04										

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04						
								S	M	T	W	T		
174		Early Voting MBBs to Tally	0.5 hrs	Tue 8/10/04	Tue 8/10/04									
175		Election Day MBBs to Tally and Rally	2 hrs	Tue 8/10/04	Tue 8/10/04									
176		Provisional Ballot MBBs to Tally	0.5 hrs	Sun 8/22/04	Sun 8/22/04									
177		Generate Reports	13 days	Tue 8/10/04	Sun 8/22/04									
178		Write Election Data to CD	13 days	Tue 8/10/04	Sun 8/22/04	177SS								
179		<b>Payment Milestone 3</b>	1 day	Wed 8/11/04	Wed 8/11/04									
180		<b>Post-Election Warehousing</b>	<b>4 days</b>	<b>Wed 8/11/04</b>	<b>Sat 8/14/04</b>	<b>159</b>								
181		Return all Equipment to Warehouse	4 days	Wed 8/11/04	Sat 8/14/04									
182		<b>Post-Election Review</b>	<b>12.38 days</b>	<b>Wed 8/11/04</b>	<b>Mon 8/23/04</b>									
183		Conduct Post Election Analysis	12 days	Wed 8/11/04	Sun 8/22/04									
184		Accomplish Joint Review with Customer	3 hrs	Mon 8/23/04	Mon 8/23/04	183								
185		<b>November 2, 2004 General Election</b>	<b>58 days</b>	<b>Wed 9/1/04</b>	<b>Sun 11/14/04</b>									
186		<b>Pre-Election Preparation</b>	<b>9.5 days</b>	<b>Wed 9/1/04</b>	<b>Tue 9/14/04</b>									
187		Ballot Language Certified by SOS	0 days	Wed 9/8/04	Wed 9/8/04									
188		Create BOSS Database	2 days	Wed 9/8/04	Thu 9/9/04	187								
189		Proof Ballot Content	3 hrs	Fri 9/10/04	Fri 9/10/04	188								
190		Create MBBs	3 hrs	Fri 9/10/04	Fri 9/10/04	189								
191		Round Trip Ballot Now	4 hrs	Fri 9/10/04	Mon 9/13/04	190								
192		Pre-Election L&A Tests-Ballot Now	2 hrs	Mon 9/13/04	Mon 9/13/04	191								
193		Create ballot quantities spreadsheet for Provisional, Absentee	8 hrs	Mon 9/13/04	Tue 9/14/04	192								
194		Early Voting In-Person Site layout	1 day	Mon 9/6/04	Mon 9/6/04									
195		eSlate Election Day Site Preparation	4 days	Wed 9/1/04	Mon 9/6/04									
196		<b>Absentee Voting (AV) By-Mail</b>	<b>41.25 days</b>	<b>Fri 9/10/04</b>	<b>Tue 11/2/04</b>									
197		Create Ballot Now Ballot Print Files	5 hrs	Fri 9/10/04	Mon 9/13/04	190								
198		Print Absentee Ballots	14 days	Mon 9/13/04	Fri 10/1/04	197								
199		Mail Ballots	18 days	Fri 10/1/04	Fri 10/22/04	198SF								
200		Receive Voted Ballots	23 days	Wed 10/6/04	Tue 11/2/04	199SS								
201		AV Ballot Processing, Scanning and Resolution	9 days	Sat 10/23/04	Tue 11/2/04									
202		Write AV Results to MBB	0.5 hrs	Tue 11/2/04	Tue 11/2/04									

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04						
								S	M	T	W	T		
203		<b>Ballot Now Provisional Ballot Voting</b>	<b>48.5 days</b>	<b>Tue 9/14/04</b>	<b>Sun 11/14/04</b>									
204		Create Provisional Ballot Now Ballot Print Files	1 day	Tue 9/14/04	Wed 9/15/04	193								
205		Print Provisional Ballots	4 days	Wed 9/15/04	Tue 9/21/04	204								
206		Package Provisional Ballots and add to Election Day Precinct s	5 days	Tue 9/21/04	Tue 9/28/04	205								
207		Provisional Ballot Processing, Scanning and Resolution	9 days	Wed 11/3/04	Sun 11/14/04									
208		Write Provisional Results to MBB	0.5 hrs	Sun 11/14/04	Sun 11/14/04									
209		<b>Conduct Election Worker Training</b>	<b>15.38 days</b>	<b>Wed 10/13/04</b>	<b>Sat 10/30/04</b>									
210		Early Voting In-Person Poll Officials and Workers	1 day	Wed 10/13/04	Wed 10/13/04									
211		Election Day Poll Officials and Workers	6 days	Fri 10/15/04	Thu 10/21/04									
212		Central Counting Staff	3 hrs	Sat 10/30/04	Sat 10/30/04	219								
213		AV Ballot Processing and Resolution Team	2 hrs	Fri 10/22/04	Fri 10/22/04									
214		<b>Early Voting In-Person (EV IP)</b>	<b>20 days</b>	<b>Mon 10/11/04</b>	<b>Tue 11/2/04</b>									
215		Marshall Equipment for EV IP Locations	0.5 days	Mon 10/11/04	Mon 10/11/04									
216		Deploy Equipment to EV IP polling places	0.5 days	Fri 10/15/04	Fri 10/15/04									
217		Setup Polls	1 hr	Fri 10/15/04	Fri 10/15/04	216								
218		Disburse Supplies	1 day	Fri 10/15/04	Sat 10/16/04	217								
219		Conduct Early Voting	11 days	Mon 10/18/04	Fri 10/29/04									
220		Secure Polls	0.5 hrs	Fri 10/29/04	Fri 10/29/04									
221		Secure Ballot Cans at Central Count Station	1 hr	Fri 10/29/04	Fri 10/29/04									
222		Return Equipment to Warehouse	1 hr	Fri 10/29/04	Fri 10/29/04									
223		EV Ballot Processing, Scanning and Resolution	3 days	Sat 10/30/04	Tue 11/2/04									
224		<b>Election Day (ED) Voting</b>	<b>8 days</b>	<b>Mon 10/25/04</b>	<b>Tue 11/2/04</b>									
225		Marshal ED Equipment	3 days	Mon 10/25/04	Wed 10/27/04									
226		Deploy Equipment to ED polling places	5 days	Wed 10/27/04	Mon 11/1/04									
227		Disburse Supplies	3 days	Fri 10/29/04	Mon 11/1/04									
228		Setup Polls	0.5 hrs	Tue 11/2/04	Tue 11/2/04	229FF								
229		Conduct ED Voting	1 day	Tue 11/2/04	Tue 11/2/04									
230		Close Polls	8 hrs	Tue 11/2/04	Tue 11/2/04									
231		Secure Polls	8 hrs	Tue 11/2/04	Tue 11/2/04									


Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

ID	i	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 11, '04						
								S	M	T	W	T		
232		Receive voted ballots at Central Count Station	8 hrs	Tue 11/2/04	Tue 11/2/04									
233		Process voted ballots at Rally Station	1 hr	Tue 11/2/04	Tue 11/2/04									
234		<b>Central Counting Station Operations</b>	<b>18 days</b>	<b>Sat 10/23/04</b>	<b>Sun 11/14/04</b>									
235		Set-Up Central Count Station and Rally Station	4 hrs	Sat 10/23/04	Sat 10/23/04	201SS								
236		Practice Central Count Station Procedures including Rally	2 hrs	Sat 10/23/04	Sat 10/23/04	235								
237		<b>Tabulate Election Results</b>	<b>9.06 days</b>	<b>Tue 11/2/04</b>	<b>Sun 11/14/04</b>	<b>219</b>								
238		AV MBBs to Tally	0.2 hrs	Tue 11/2/04	Tue 11/2/04									
239		Early Voting MBBs to Tally	0.5 hrs	Tue 11/2/04	Tue 11/2/04									
240		Election Day MBBs to Tally and Rally	2 hrs	Tue 11/2/04	Tue 11/2/04									
241		Provisional Ballot MBBs to Tally	0.5 hrs	Sun 11/14/04	Sun 11/14/04									
242		Generate Reports	10 days	Tue 11/2/04	Sun 11/14/04									
243		Write Election Data to CD	10 days	Tue 11/2/04	Sun 11/14/04	242SS								
244		<b>Payment Milestone Four</b>	<b>1 day</b>	<b>Wed 11/3/04</b>	<b>Wed 11/3/04</b>									
245		<b>Post-Election Warehousing</b>	<b>4 days</b>	<b>Wed 11/3/04</b>	<b>Mon 11/8/04</b>									
246		Return all Equipment to Warehouse	4 days	Wed 11/3/04	Mon 11/8/04									
247		<b>Post-Election Review</b>	<b>9.38 days</b>	<b>Wed 11/3/04</b>	<b>Mon 11/15/04</b>									
248		Conduct Post Election Analysis	9 days	Wed 11/3/04	Sun 11/14/04									
249		Accomplish Joint Review with Customer	3 hrs	Mon 11/15/04	Mon 11/15/04	248								
250		<b>Project Joint Review and Wrap-Up</b>	<b>0.63 days</b>	<b>Mon 11/15/04</b>	<b>Mon 11/15/04</b>									
251		Accomplish Joint Project Review and Wrap-Up	5 hrs	Mon 11/15/04	Mon 11/15/04									

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




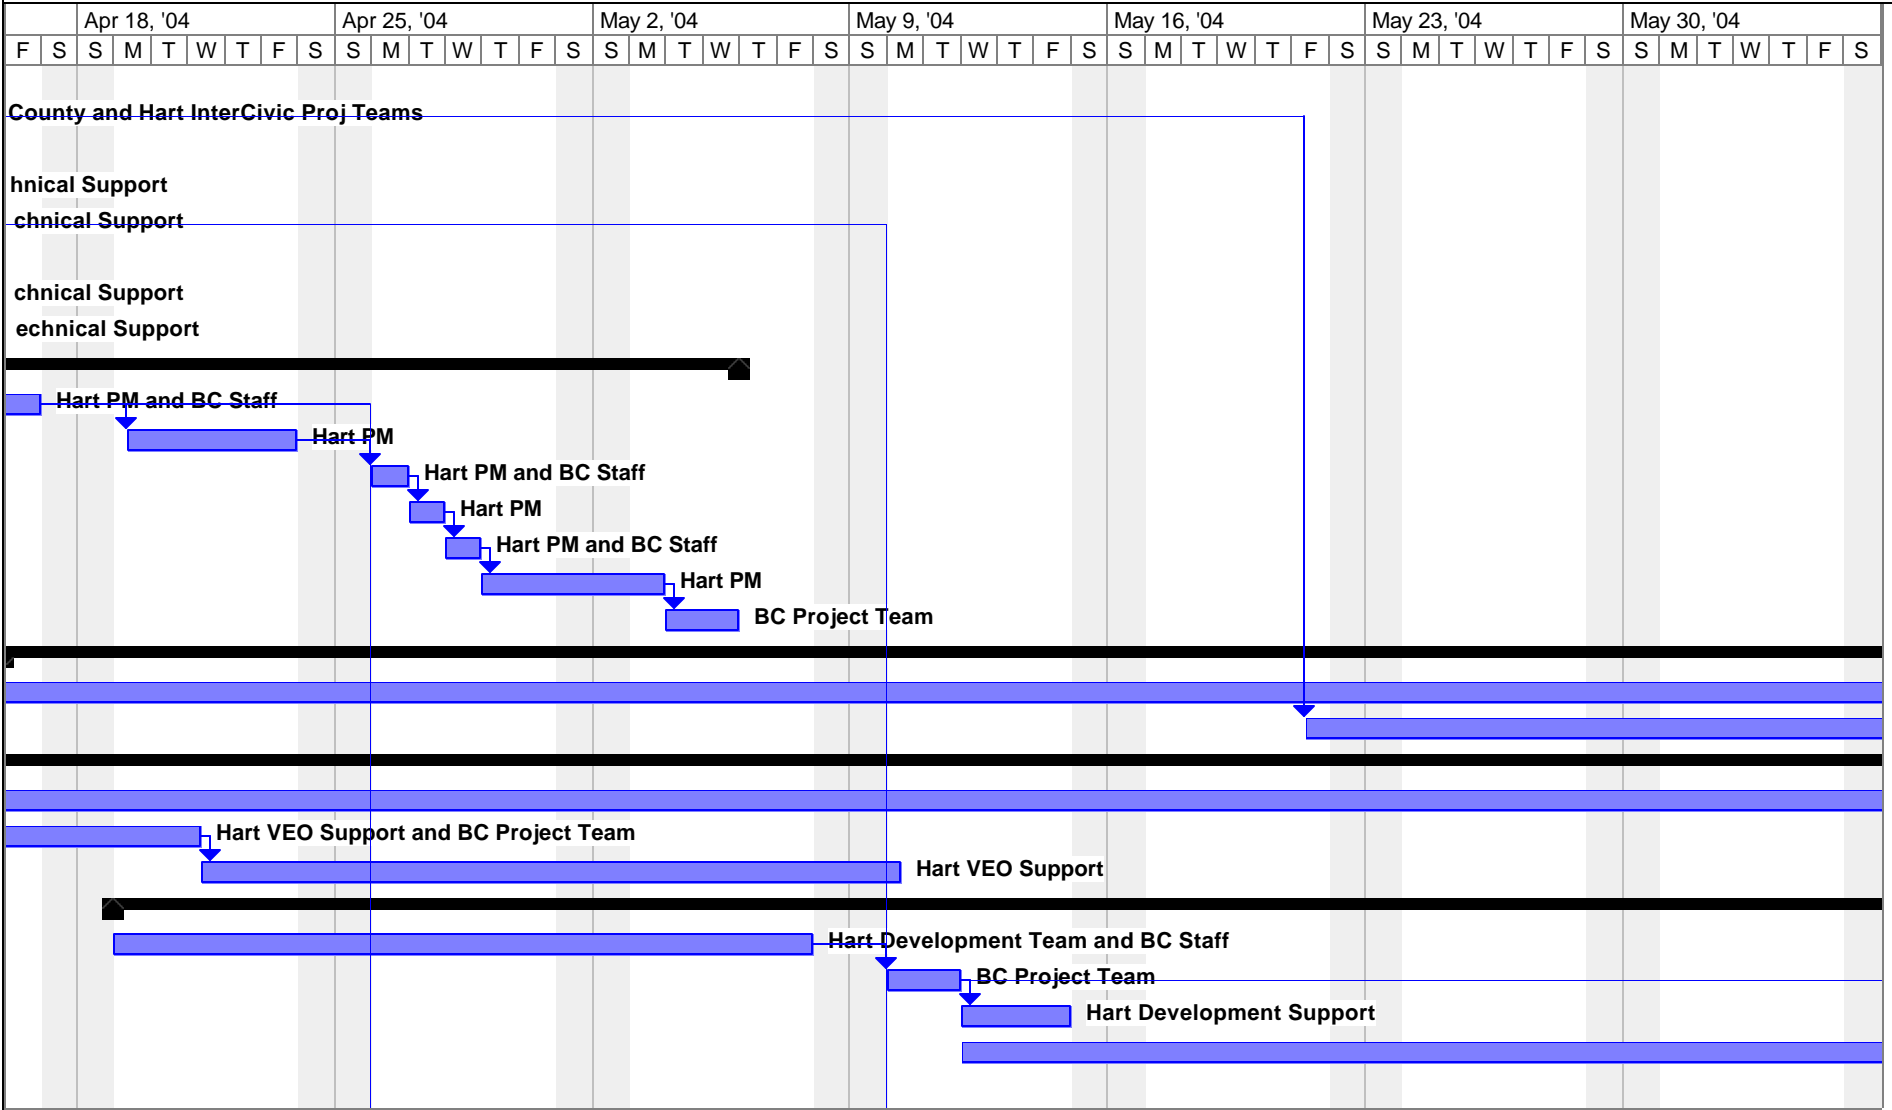

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

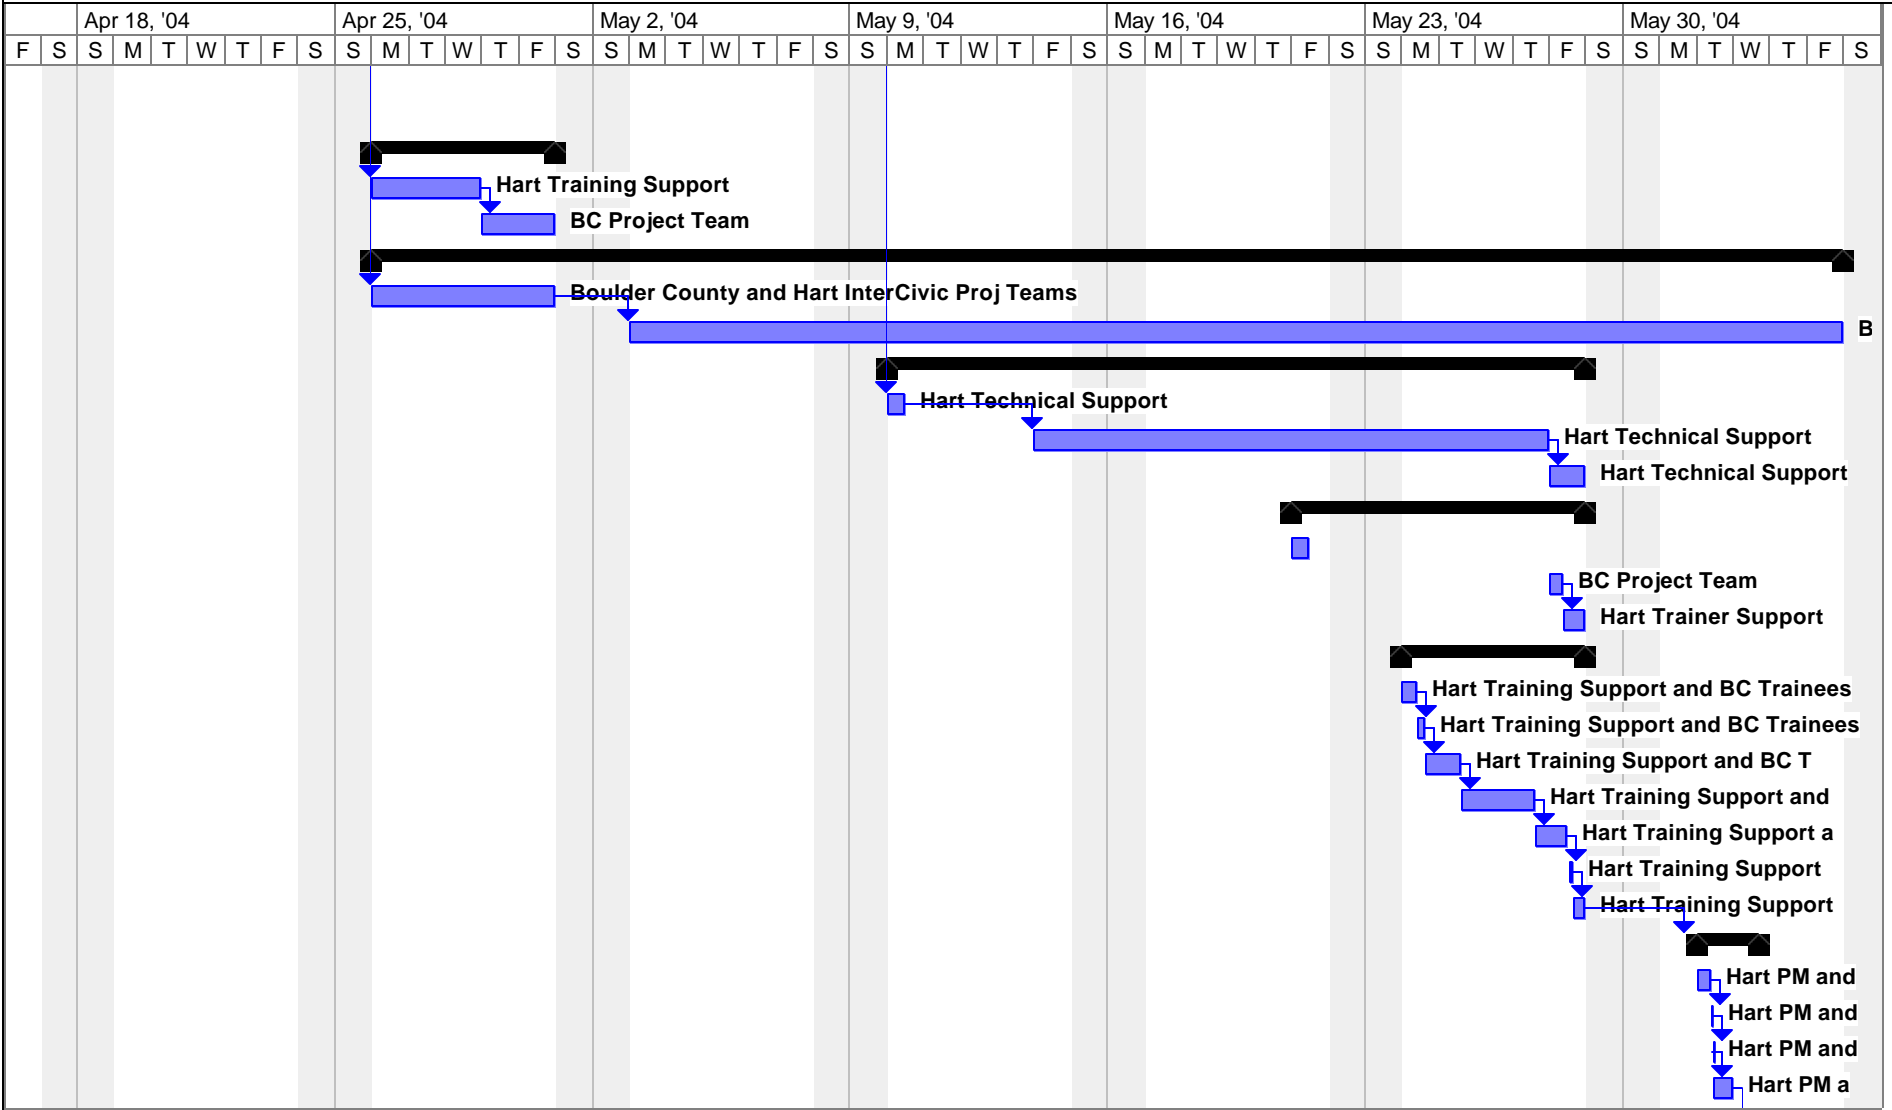

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Apr 18, '04			Apr 25, '04			May 2, '04			May 9, '04			May 16, '04			May 23, '04			May 30, '04													
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Apr 18, '04			Apr 25, '04			May 2, '04			May 9, '04			May 16, '04			May 23, '04			May 30, '04													
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		







Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Apr 18, '04		Apr 25, '04		May 2, '04		May 9, '04		May 16, '04		May 23, '04		May 30, '04																			
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		










Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation


Apr 18, '04		Apr 25, '04		May 2, '04		May 9, '04		May 16, '04		May 23, '04		May 30, '04																			
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

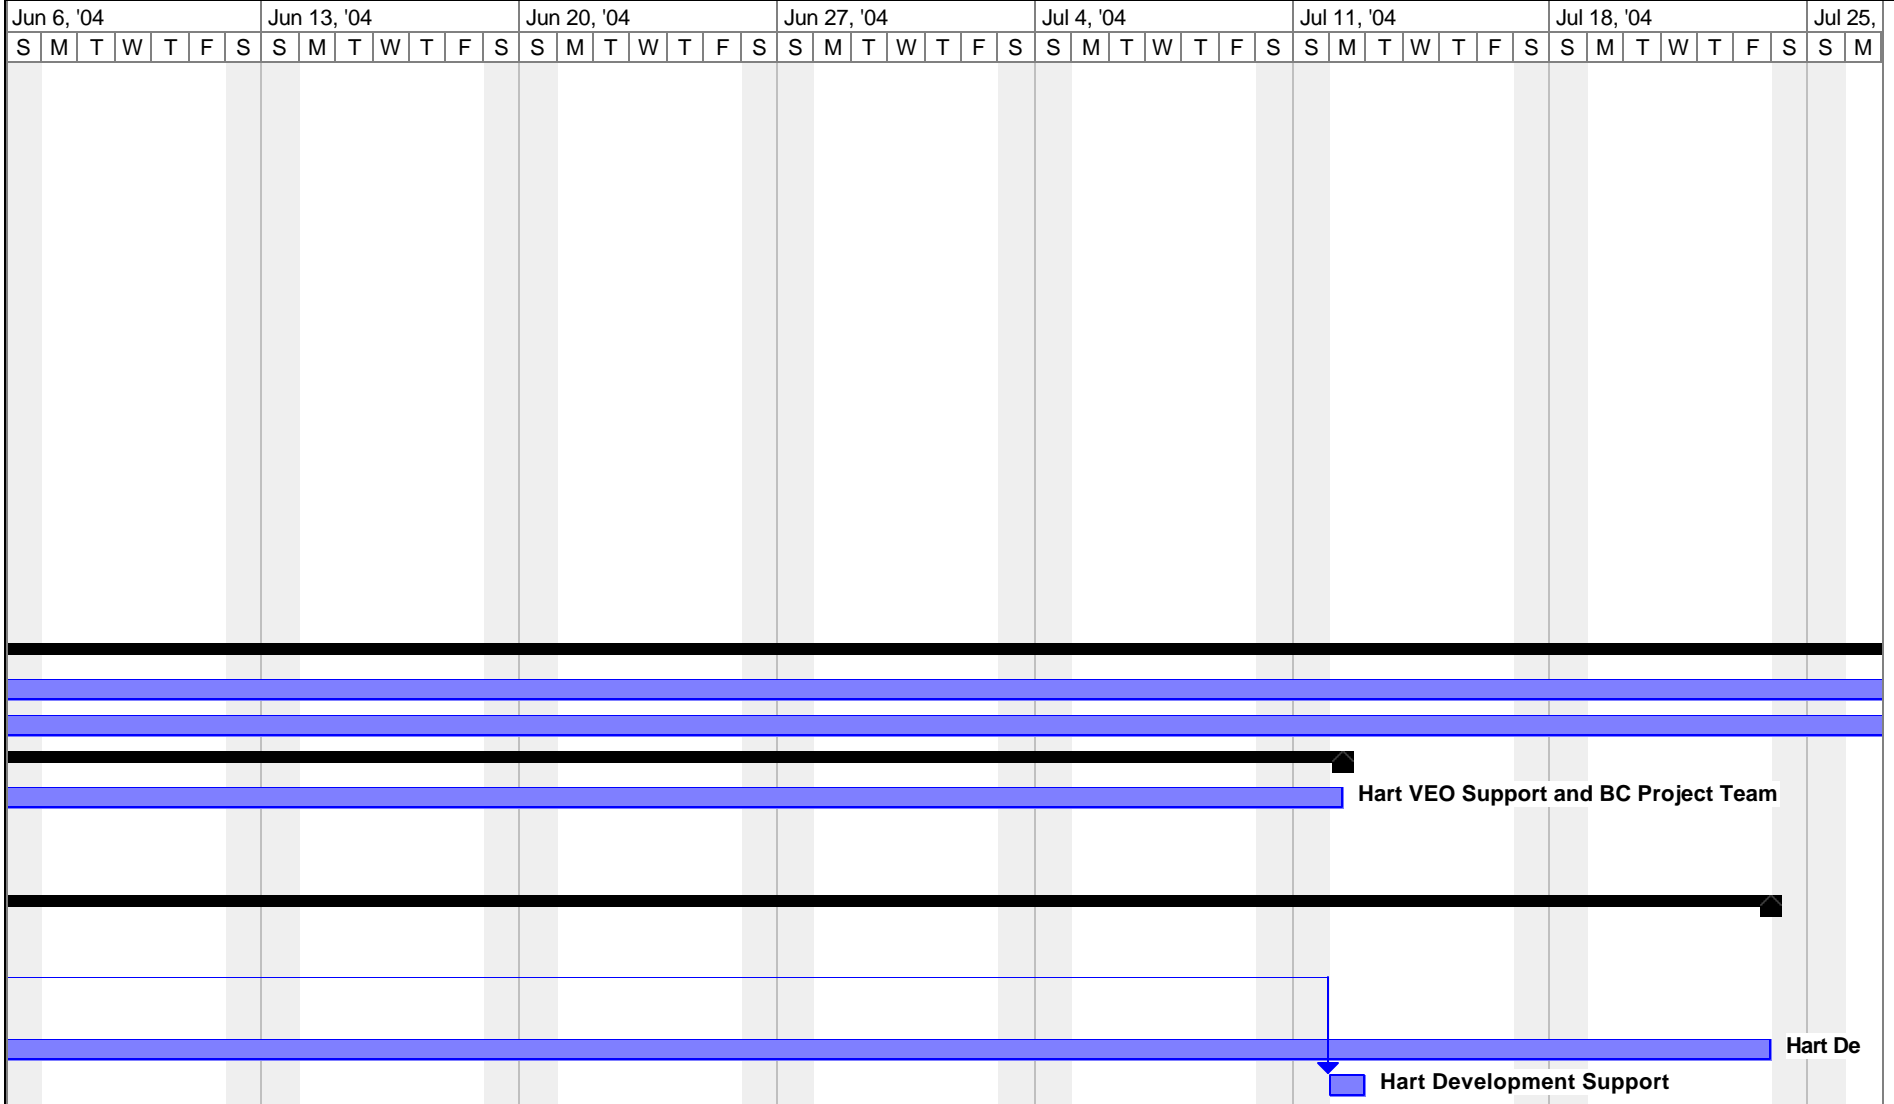

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

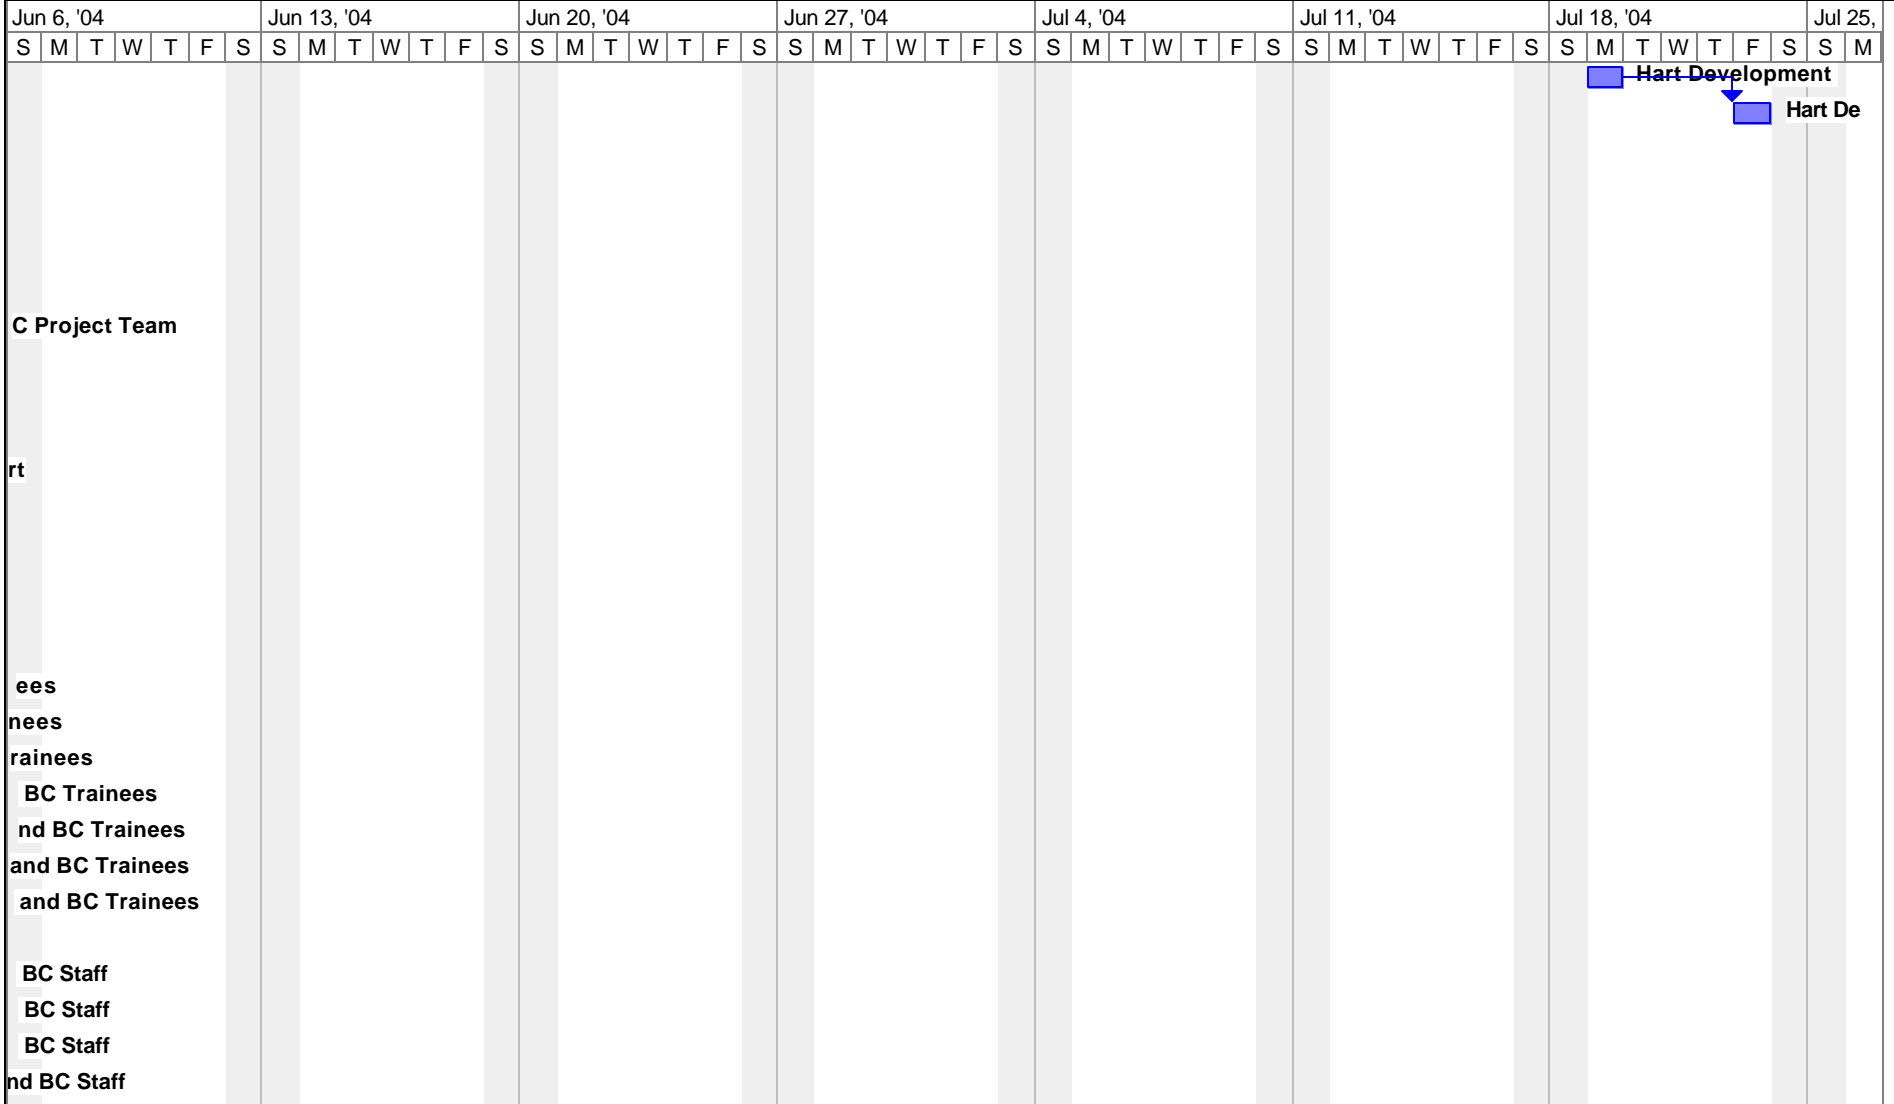

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

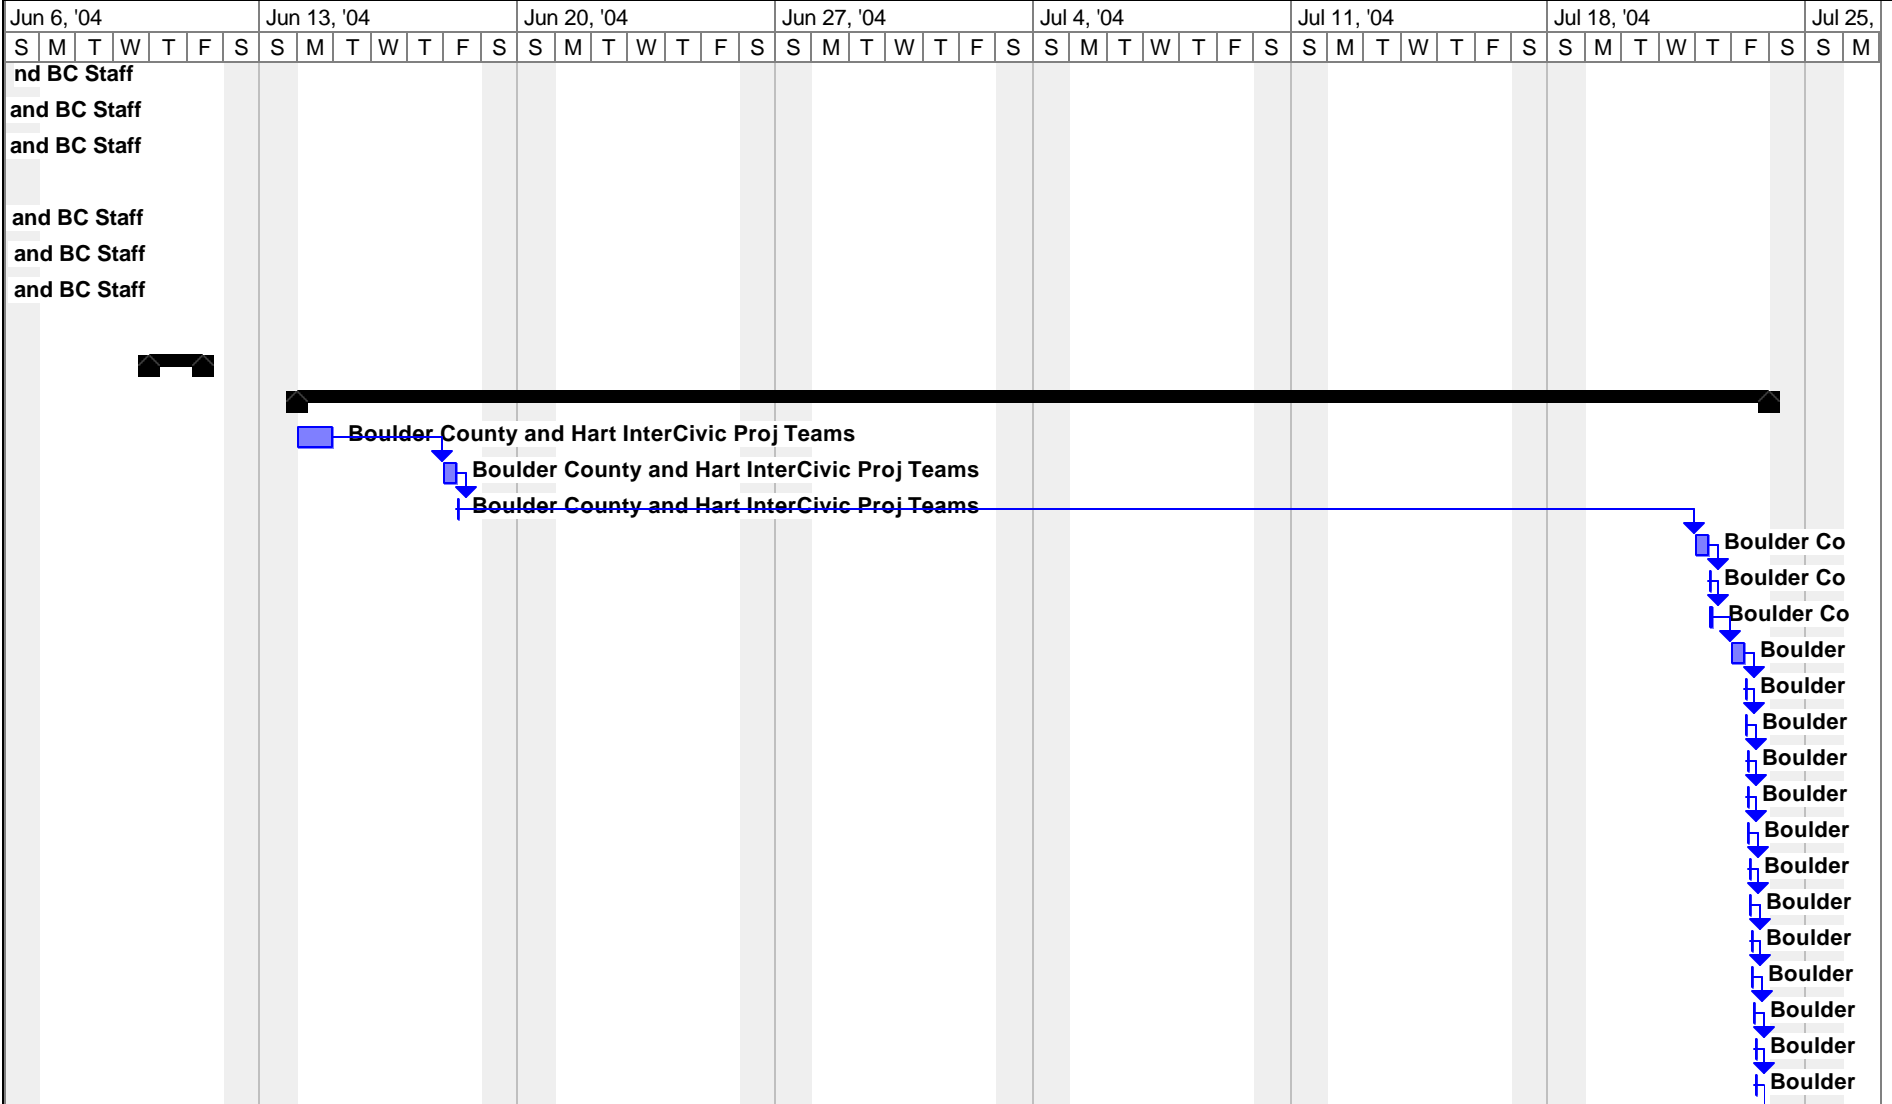

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

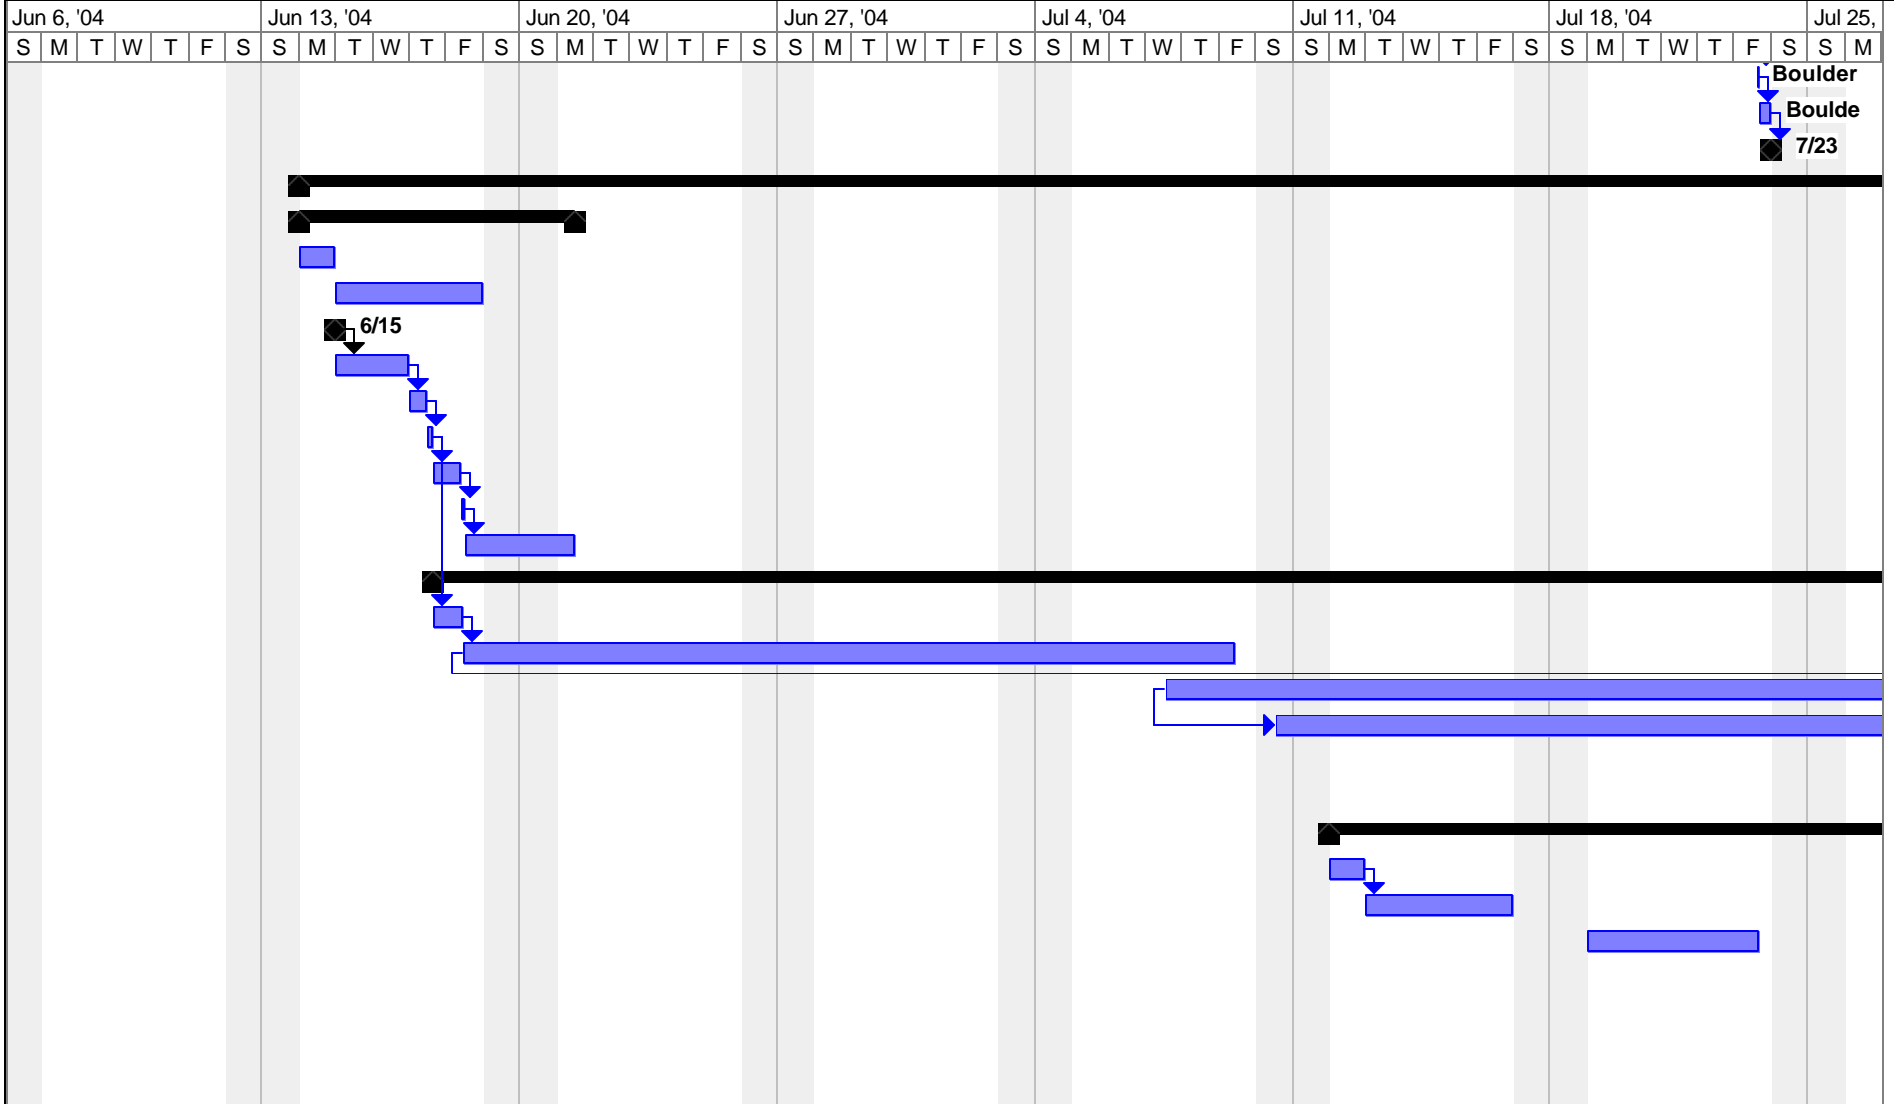







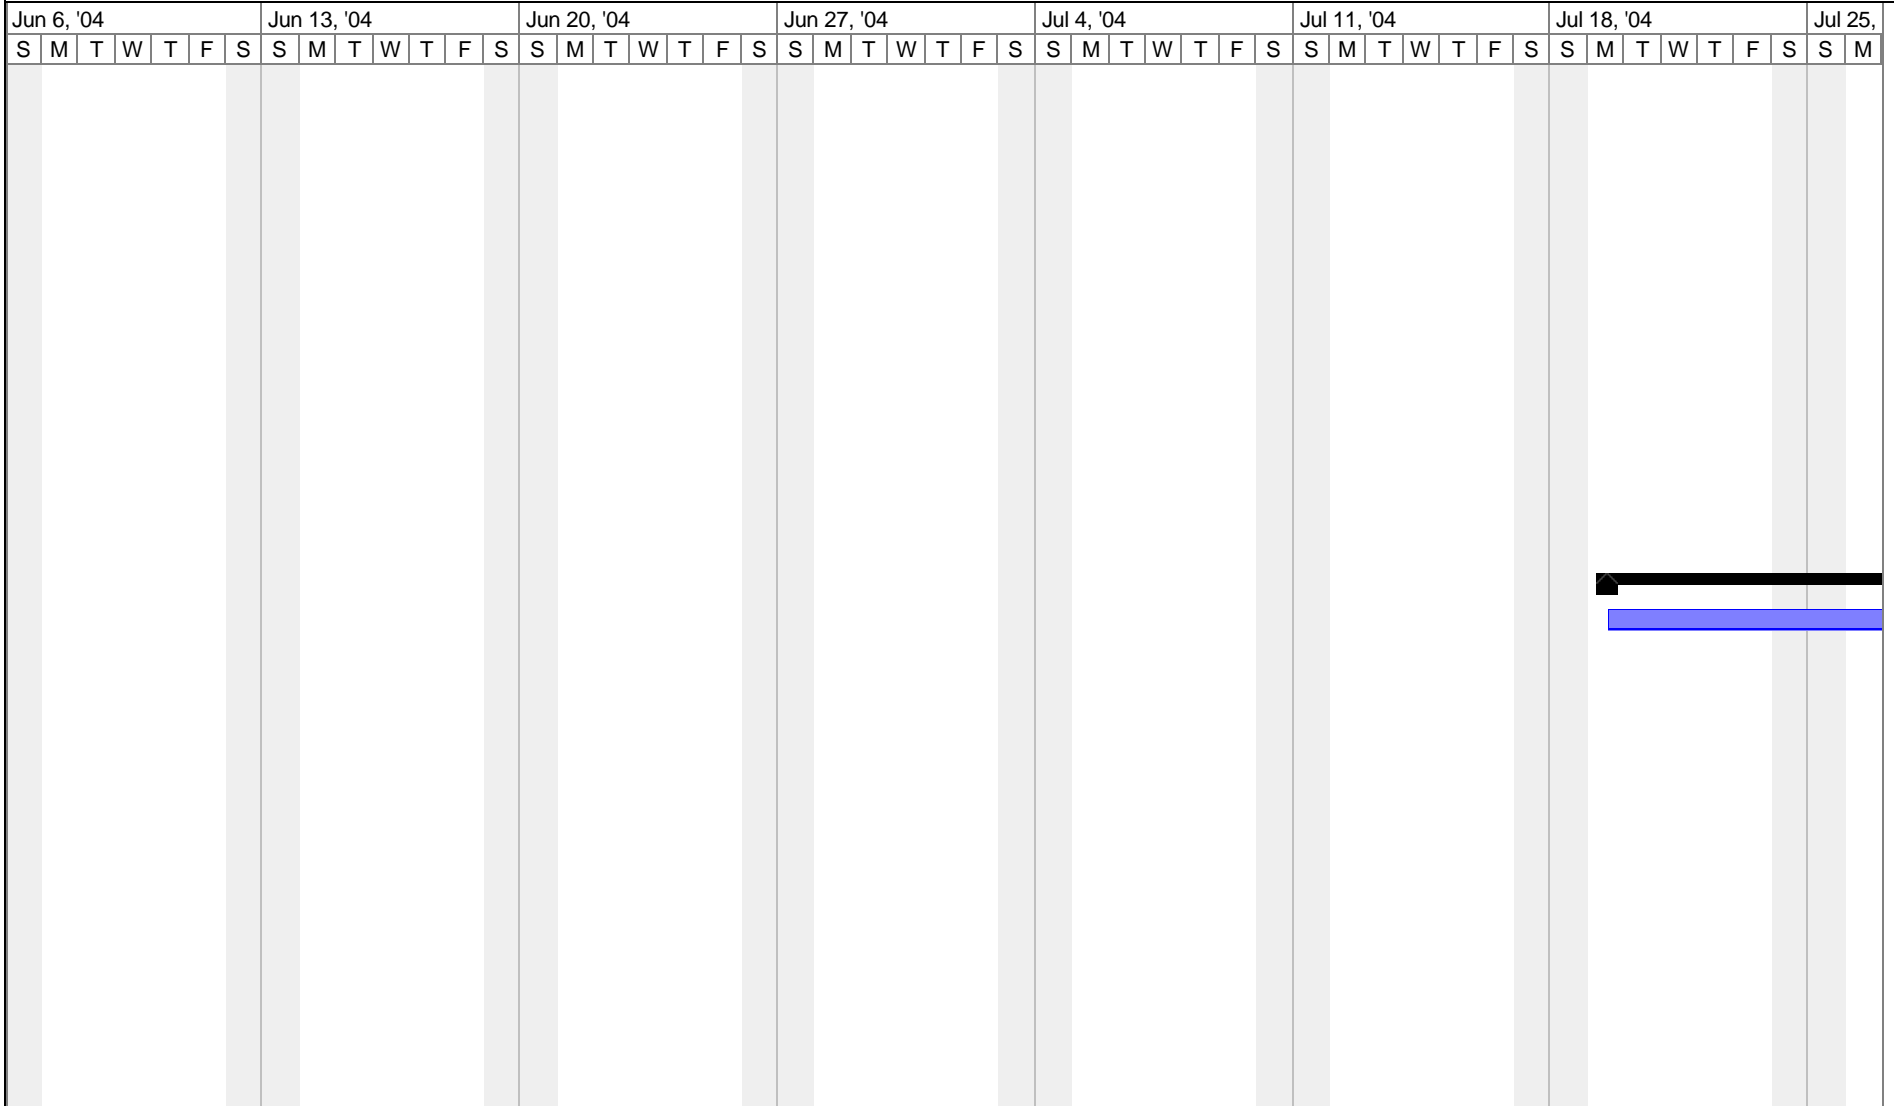


Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation












Project: Boulder County Project Plan-F  
Date: Mon 4/12/04


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation





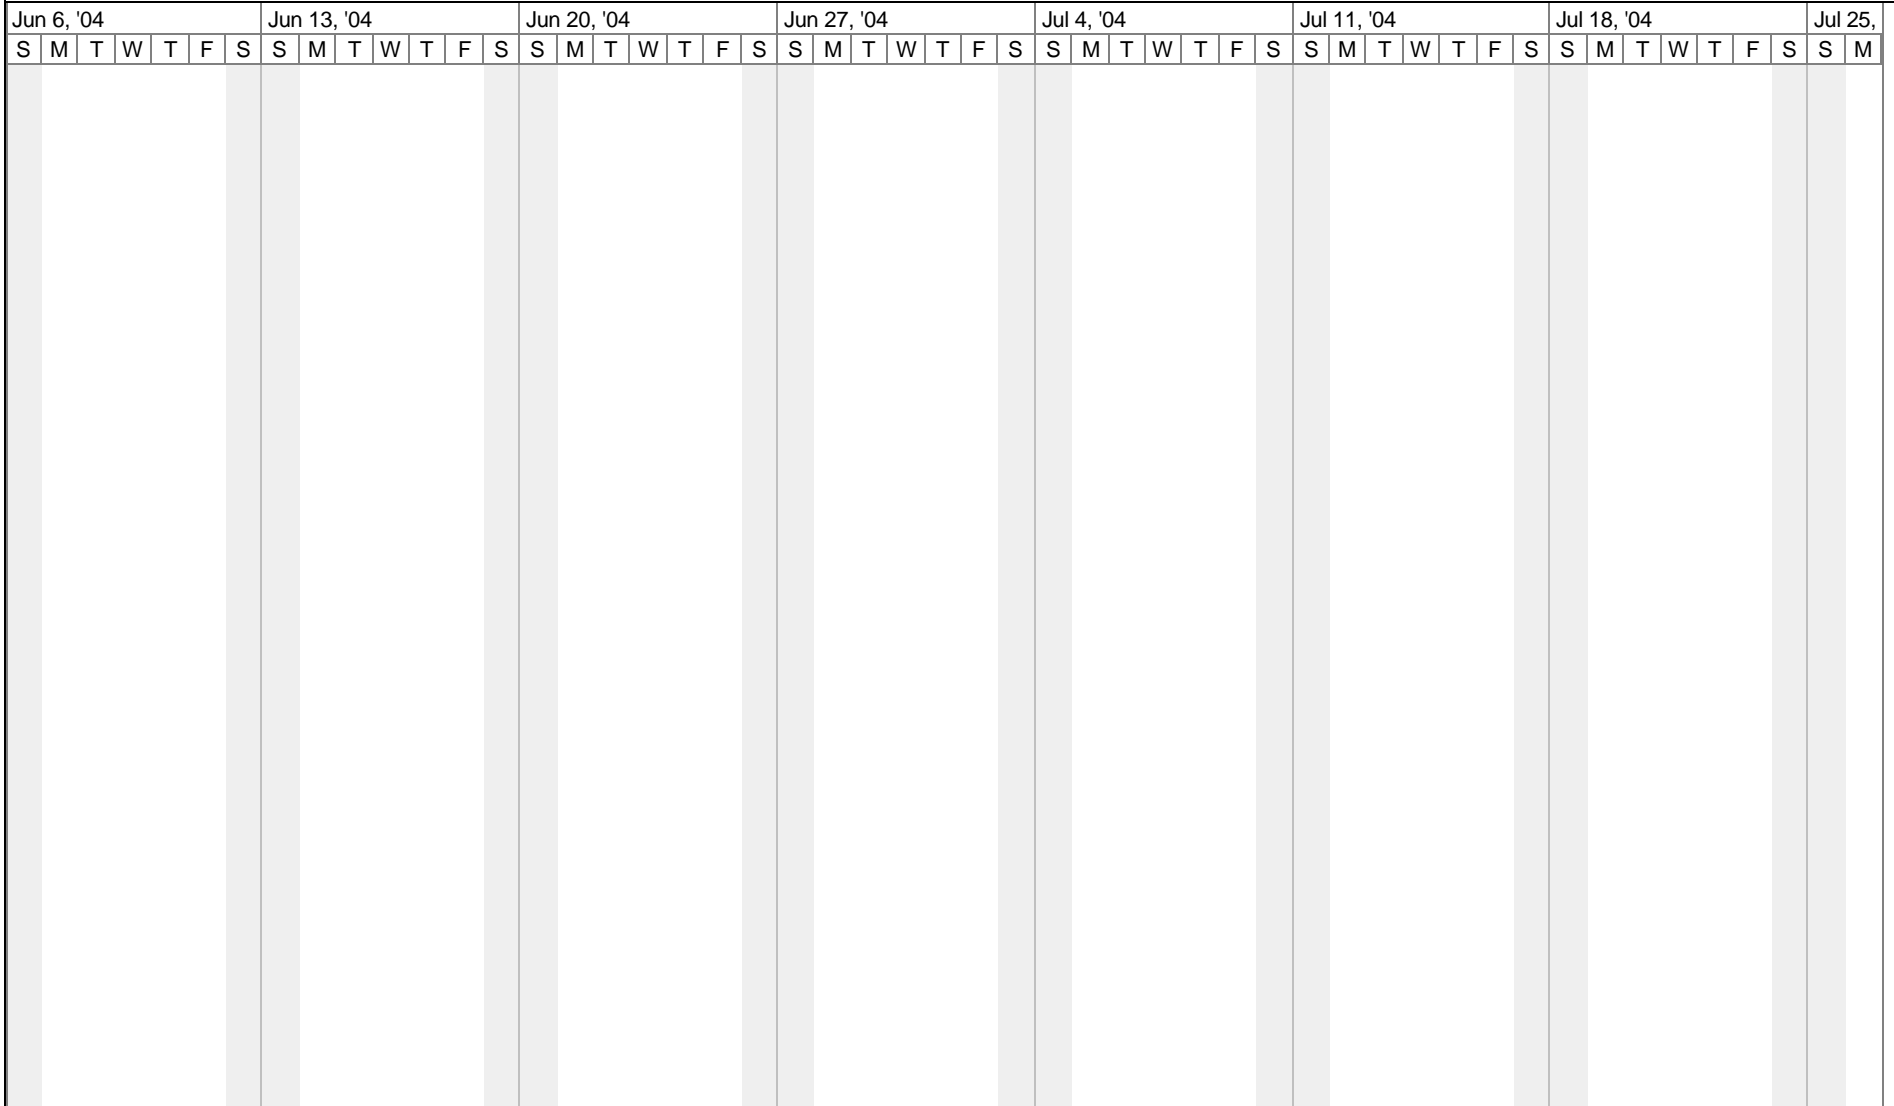

Jun 6, '04							Jun 13, '04							Jun 20, '04							Jun 27, '04							Jul 4, '04							Jul 11, '04							Jul 18, '04							Jul 25,	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation











Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Jun 6, '04							Jun 13, '04							Jun 20, '04							Jun 27, '04							Jul 4, '04							Jul 11, '04							Jul 18, '04							Jul 25,	
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation







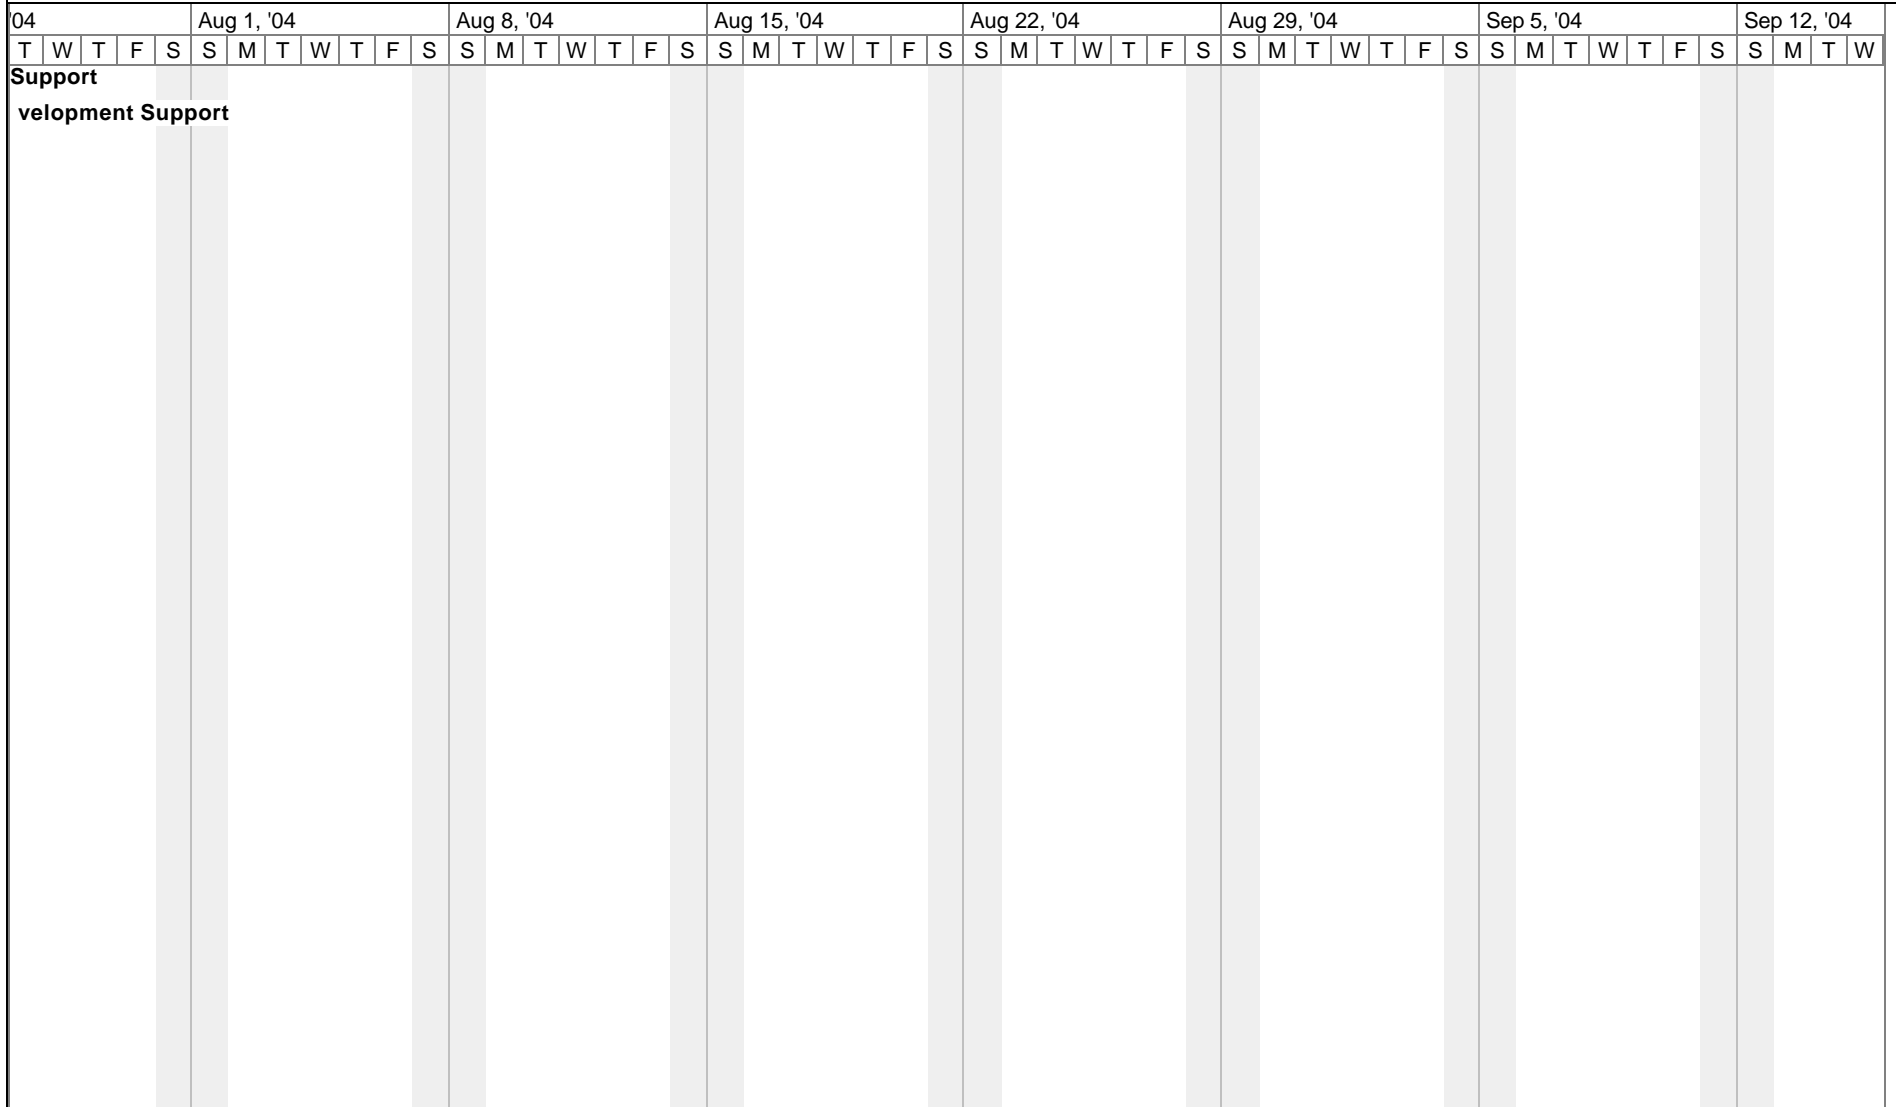


Development Support

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation




Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	






Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

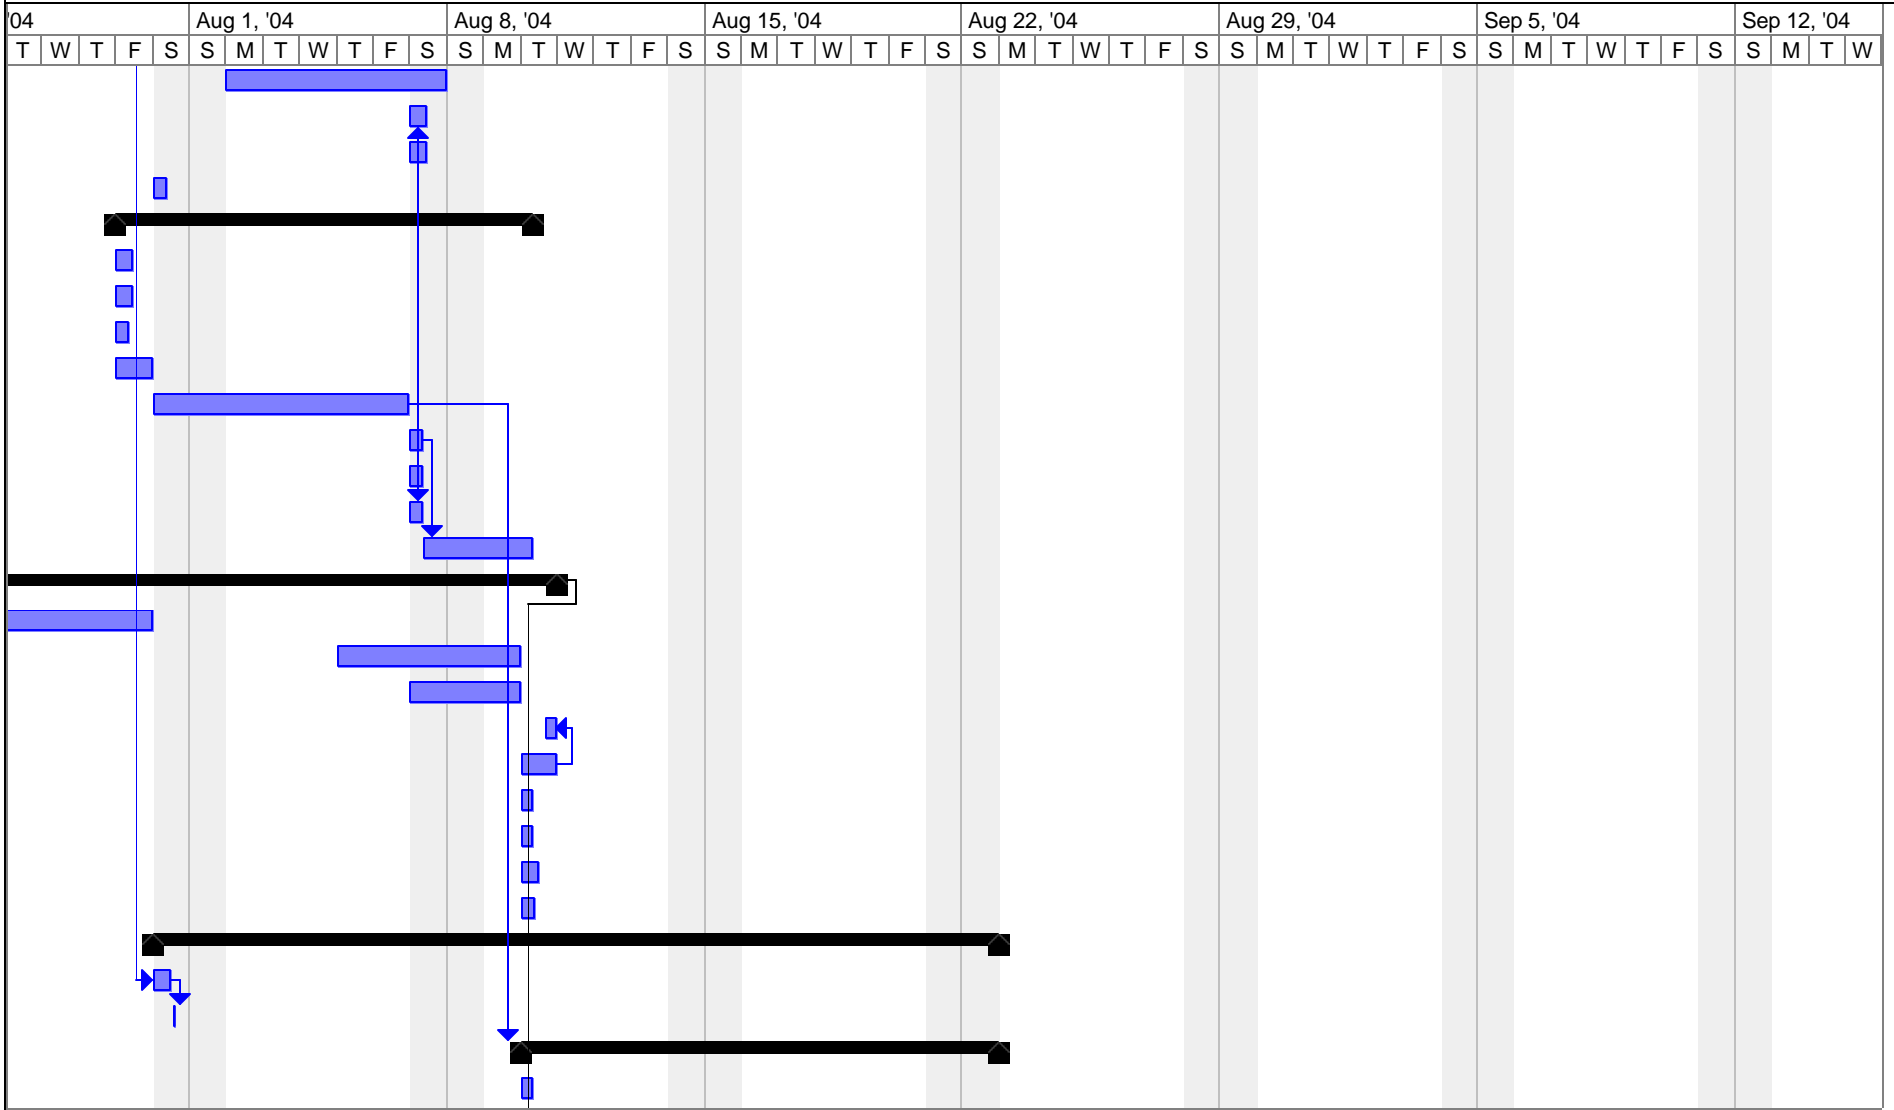

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

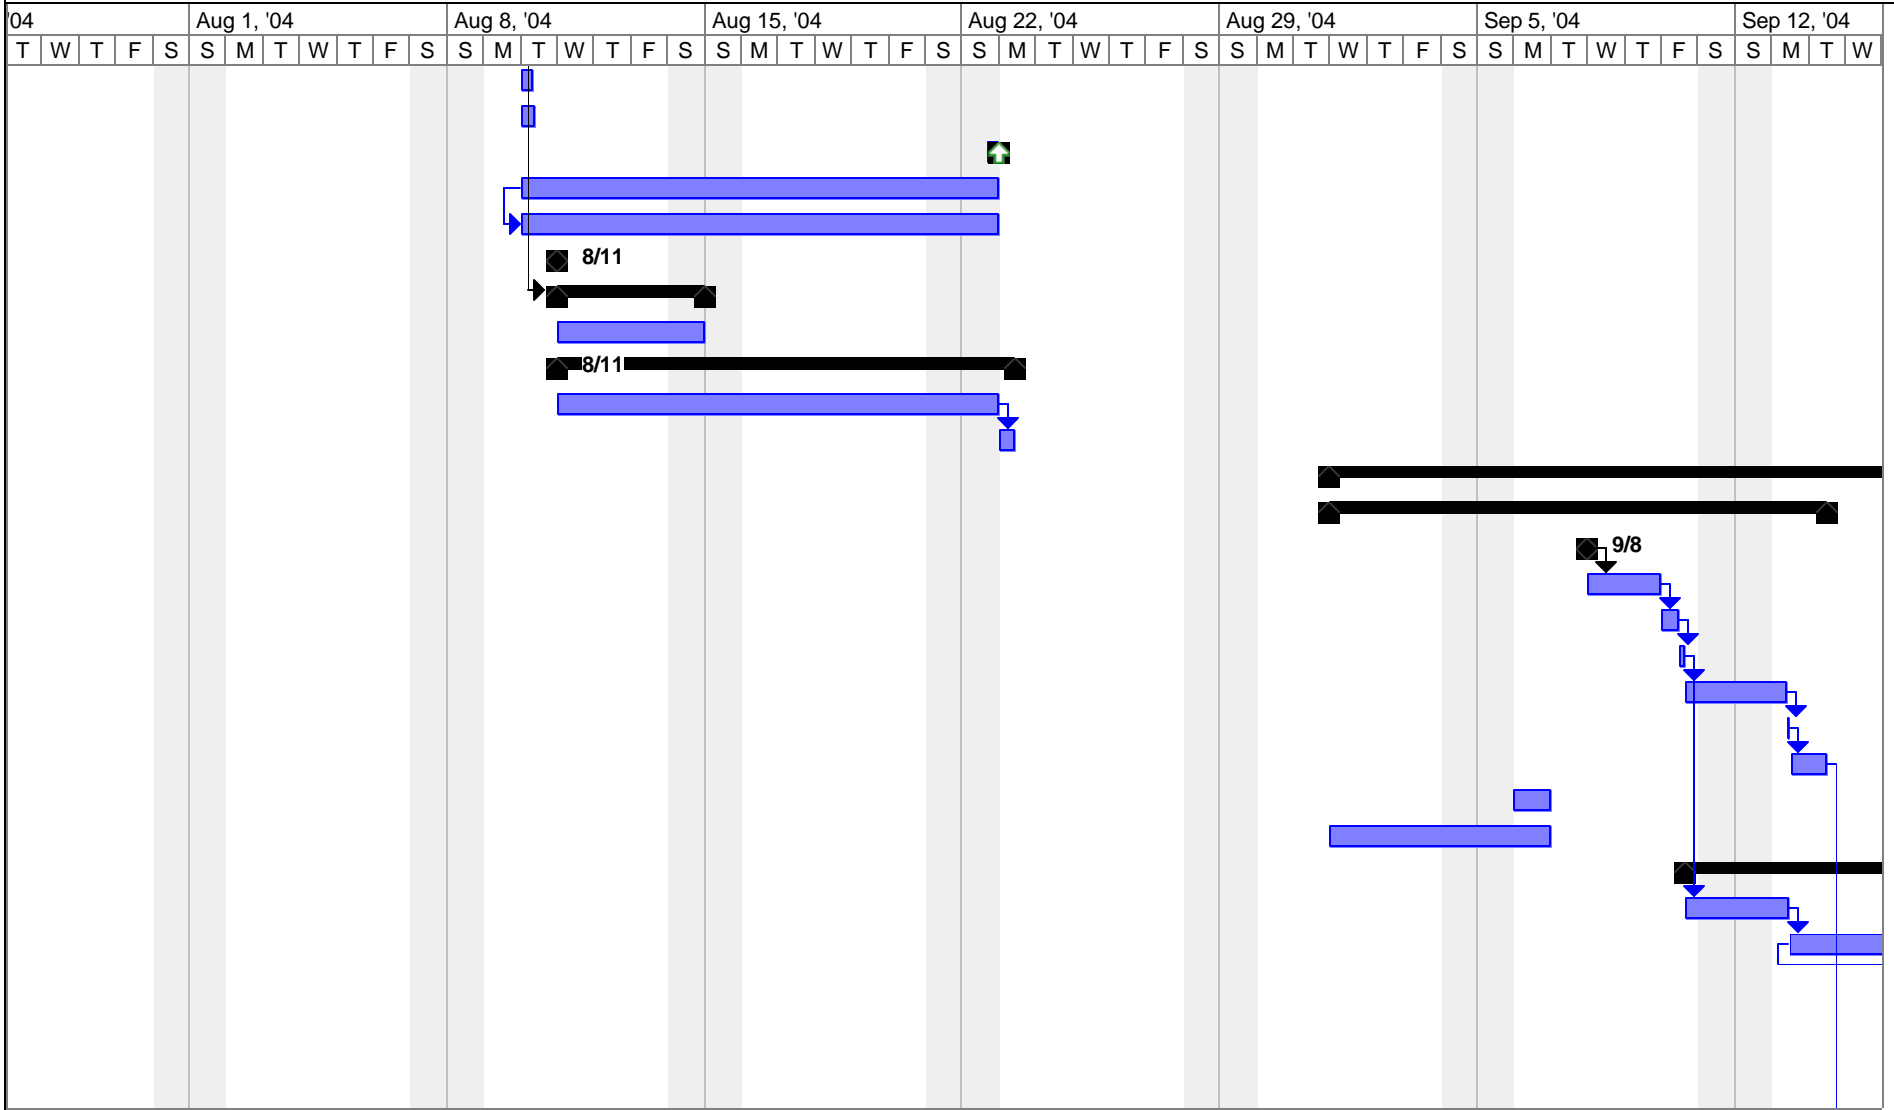

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

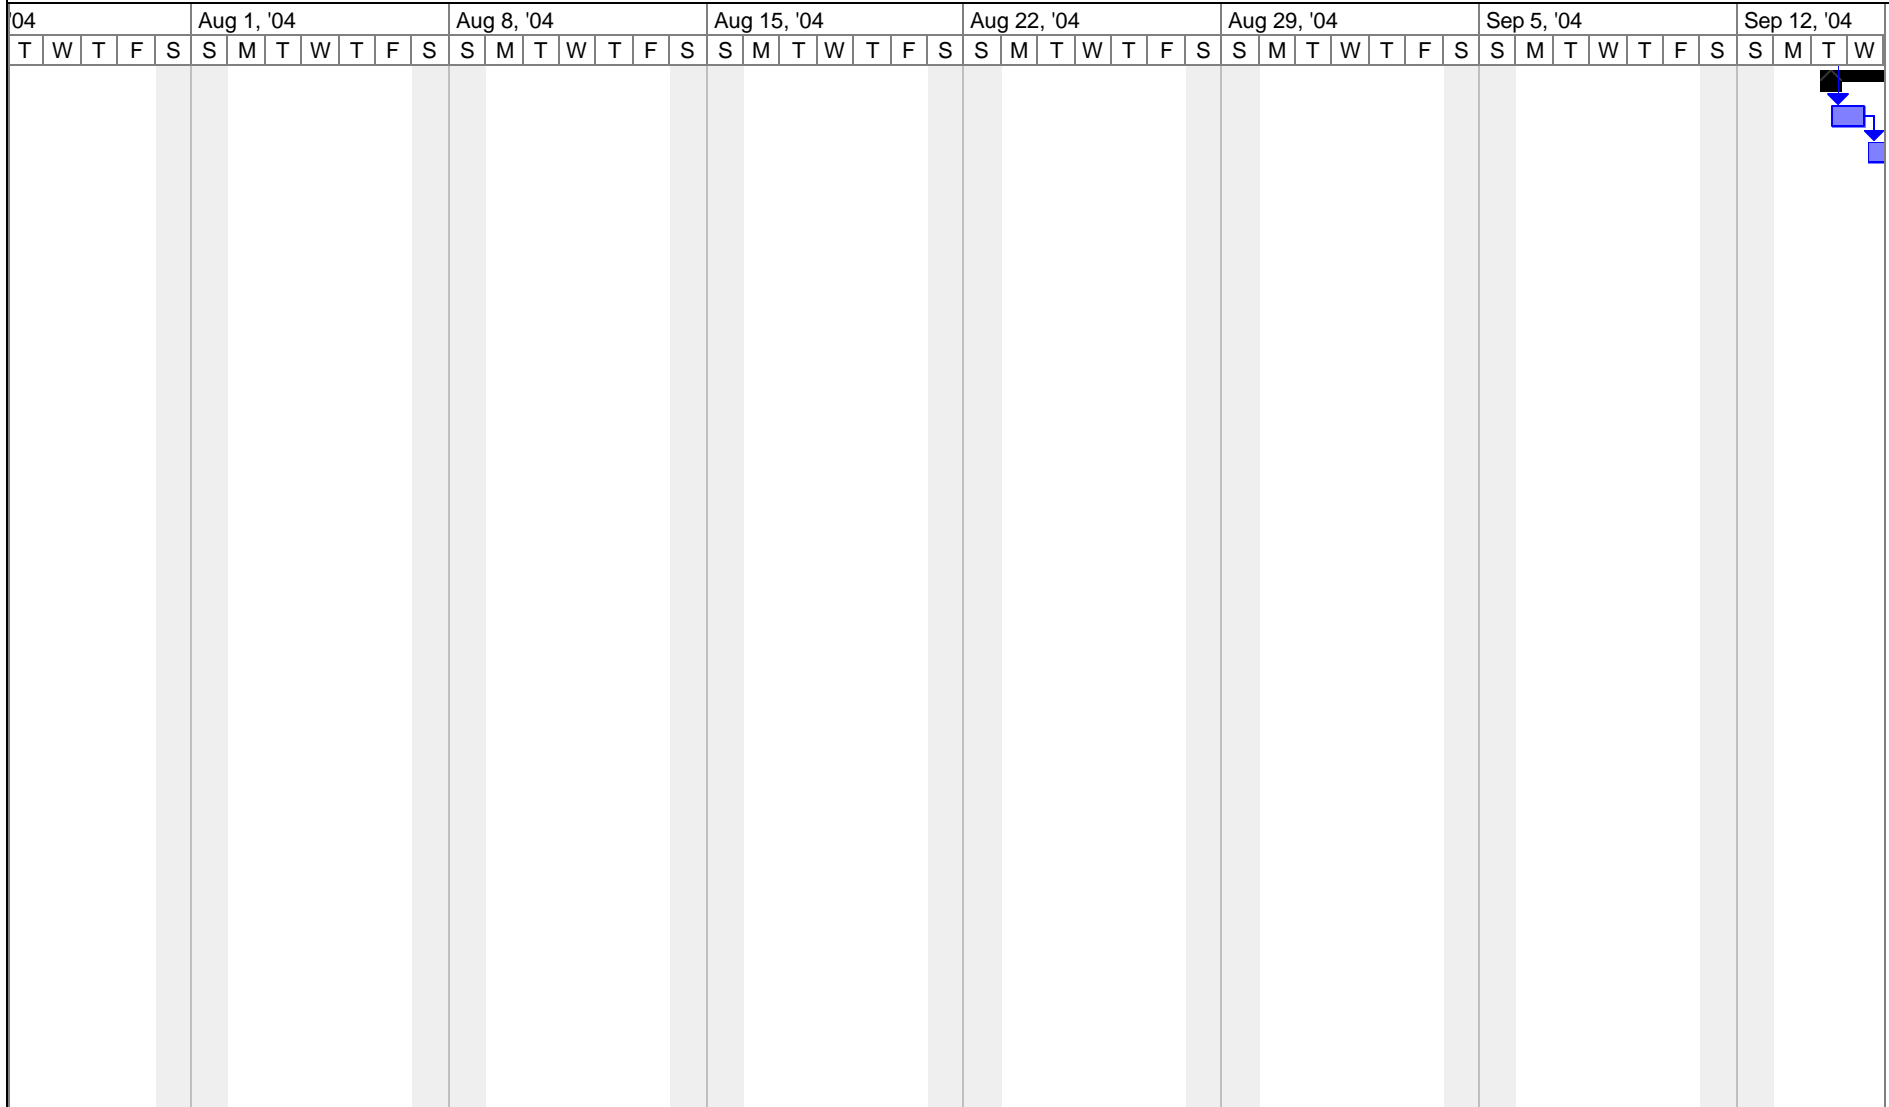






Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation




Project: Boulder County Project Plan-F  
Date: Mon 4/12/04







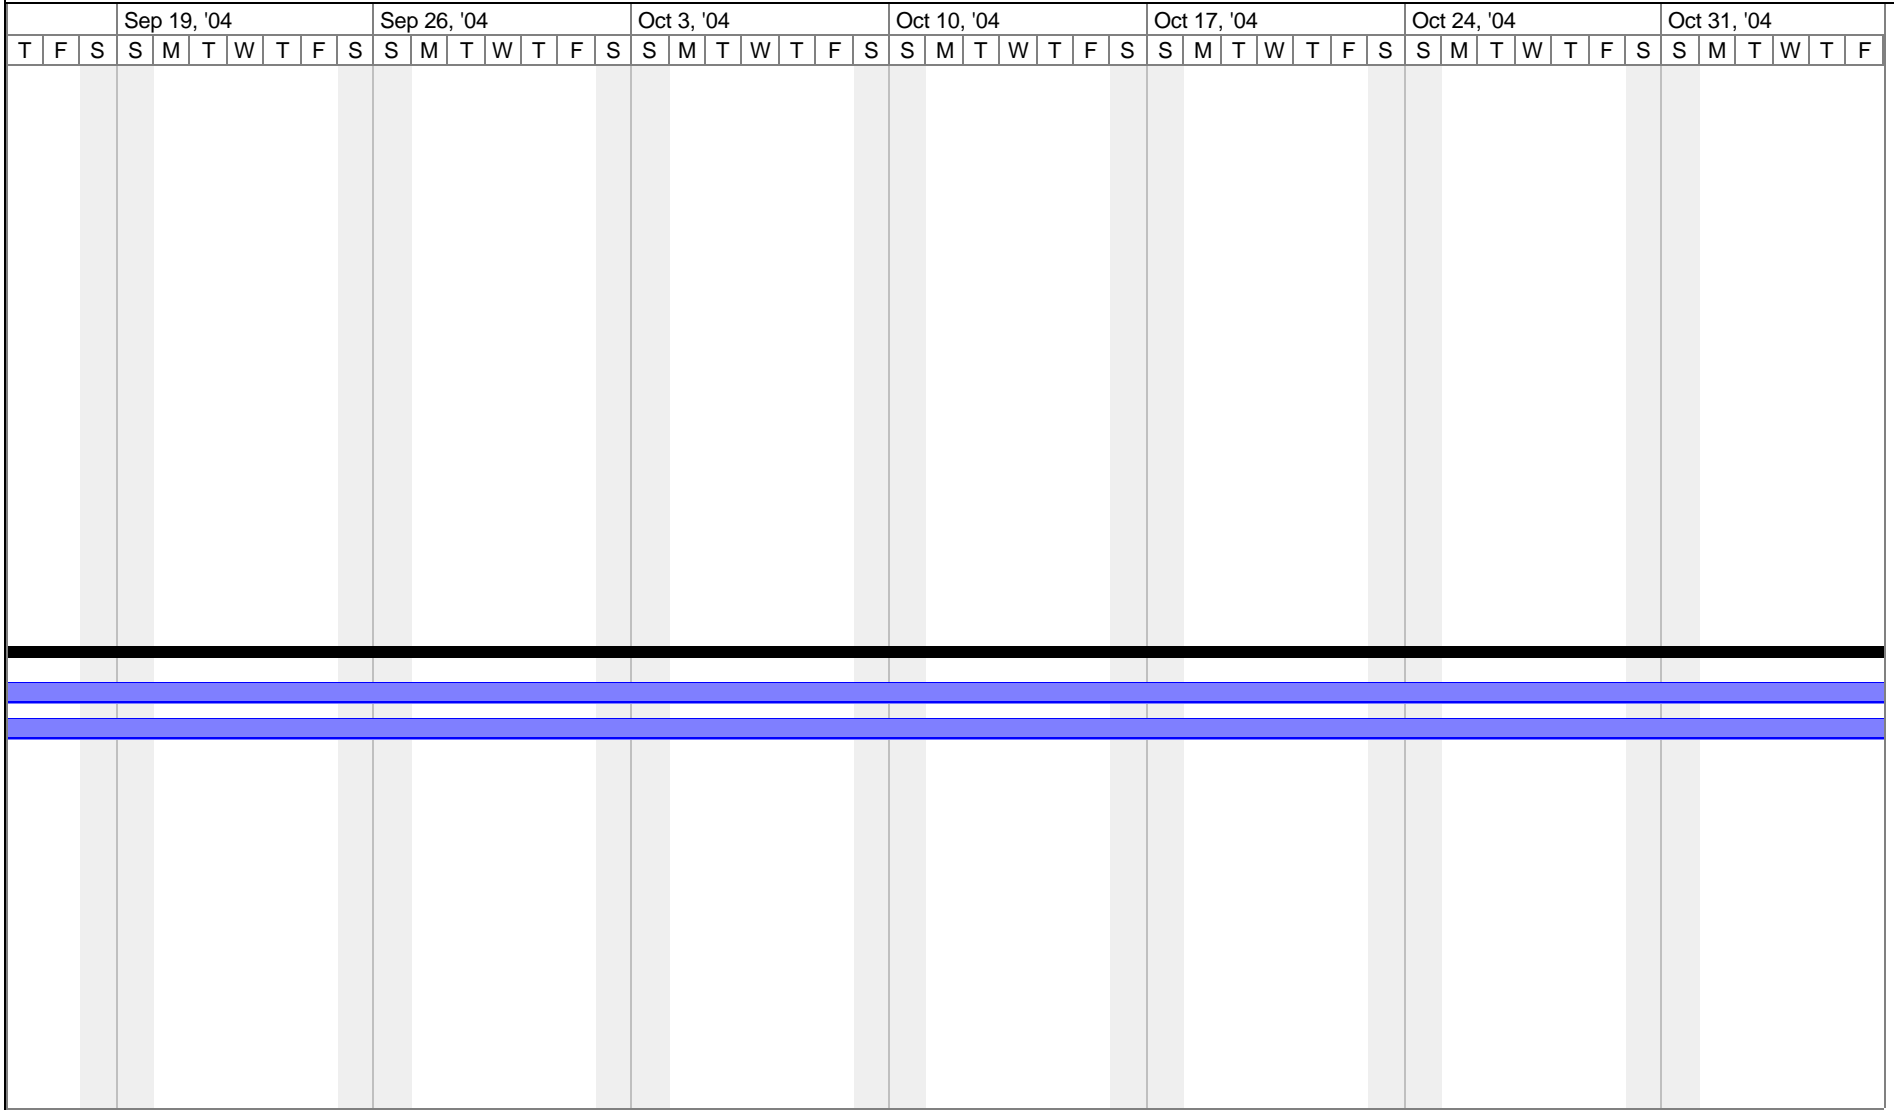

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation












Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Sep 19, '04			Sep 26, '04			Oct 3, '04			Oct 10, '04			Oct 17, '04			Oct 24, '04			Oct 31, '04																			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S








Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Sep 19, '04			Sep 26, '04			Oct 3, '04			Oct 10, '04			Oct 17, '04			Oct 24, '04			Oct 31, '04																			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	










Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Sep 19, '04			Sep 26, '04			Oct 3, '04			Oct 10, '04			Oct 17, '04			Oct 24, '04			Oct 31, '04																			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S








Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Sep 19, '04			Sep 26, '04			Oct 3, '04			Oct 10, '04			Oct 17, '04			Oct 24, '04			Oct 31, '04																			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

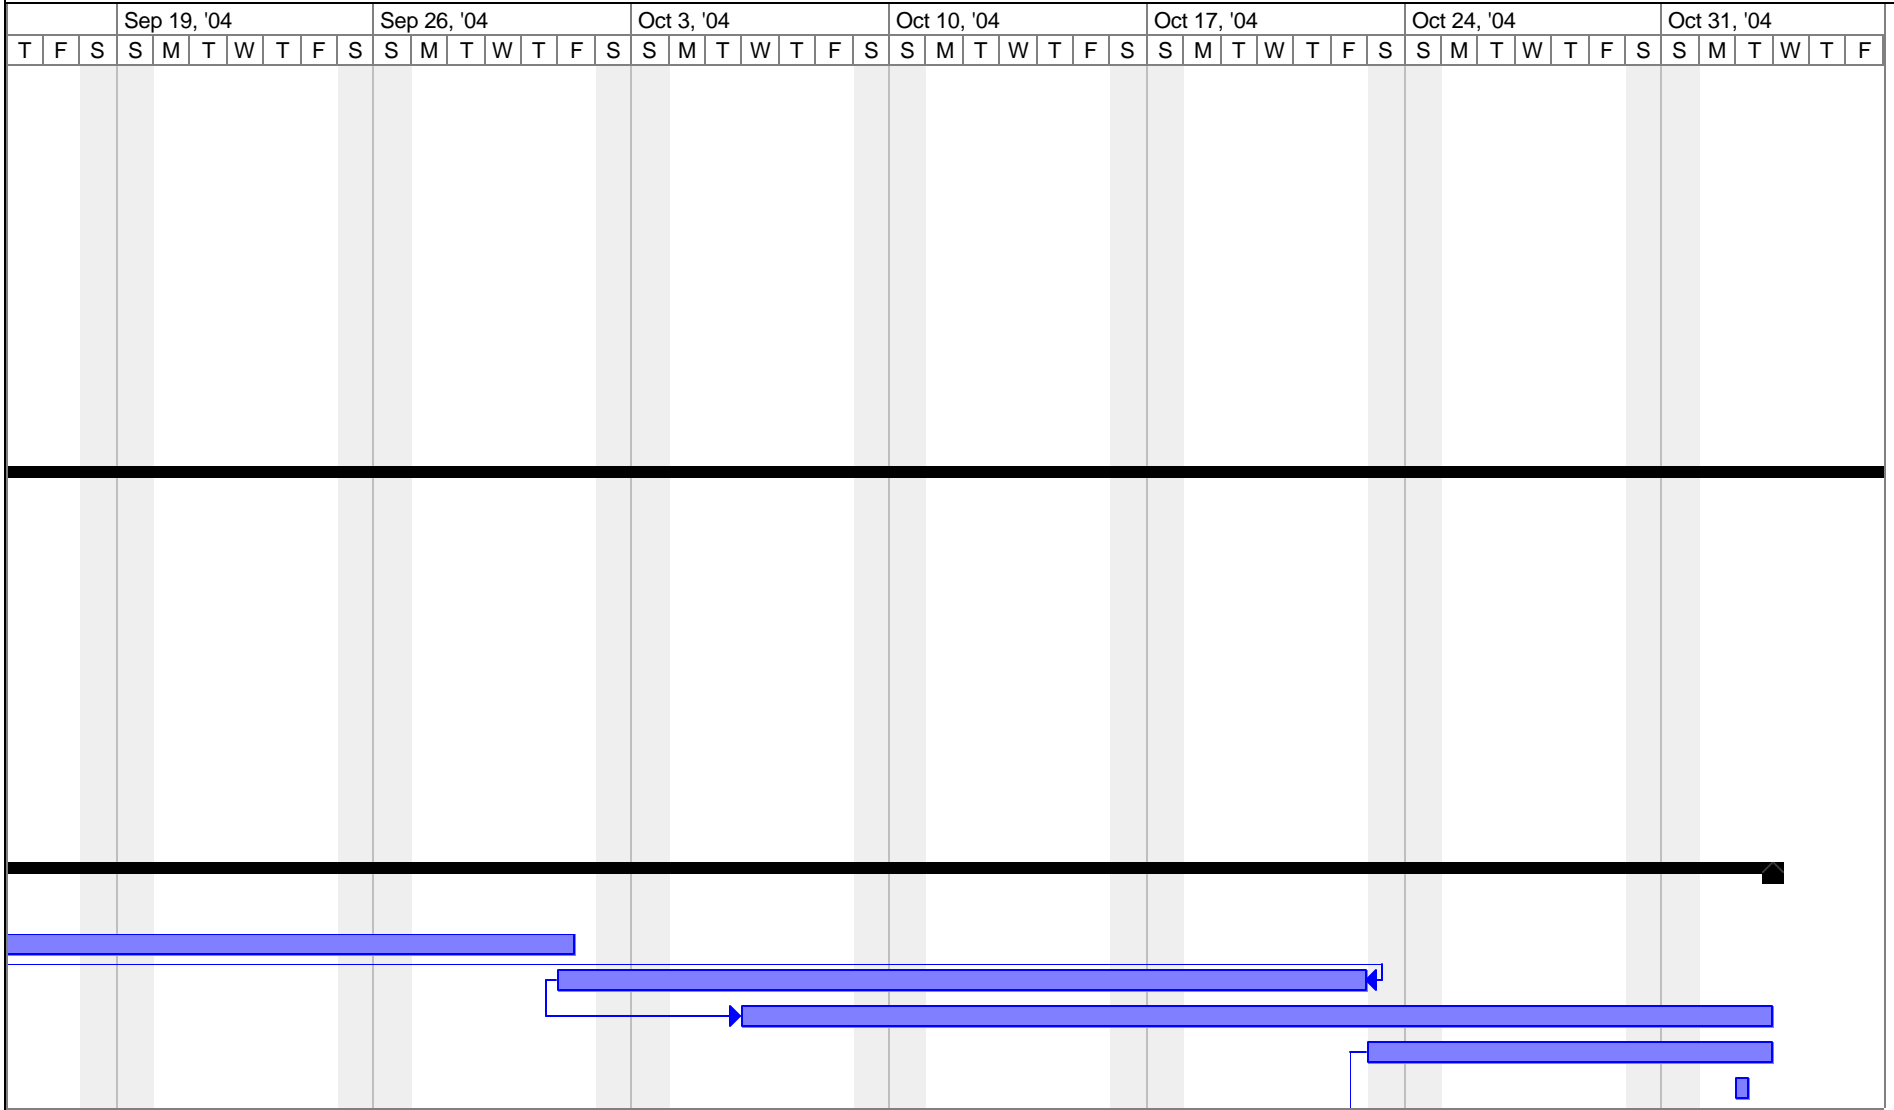

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

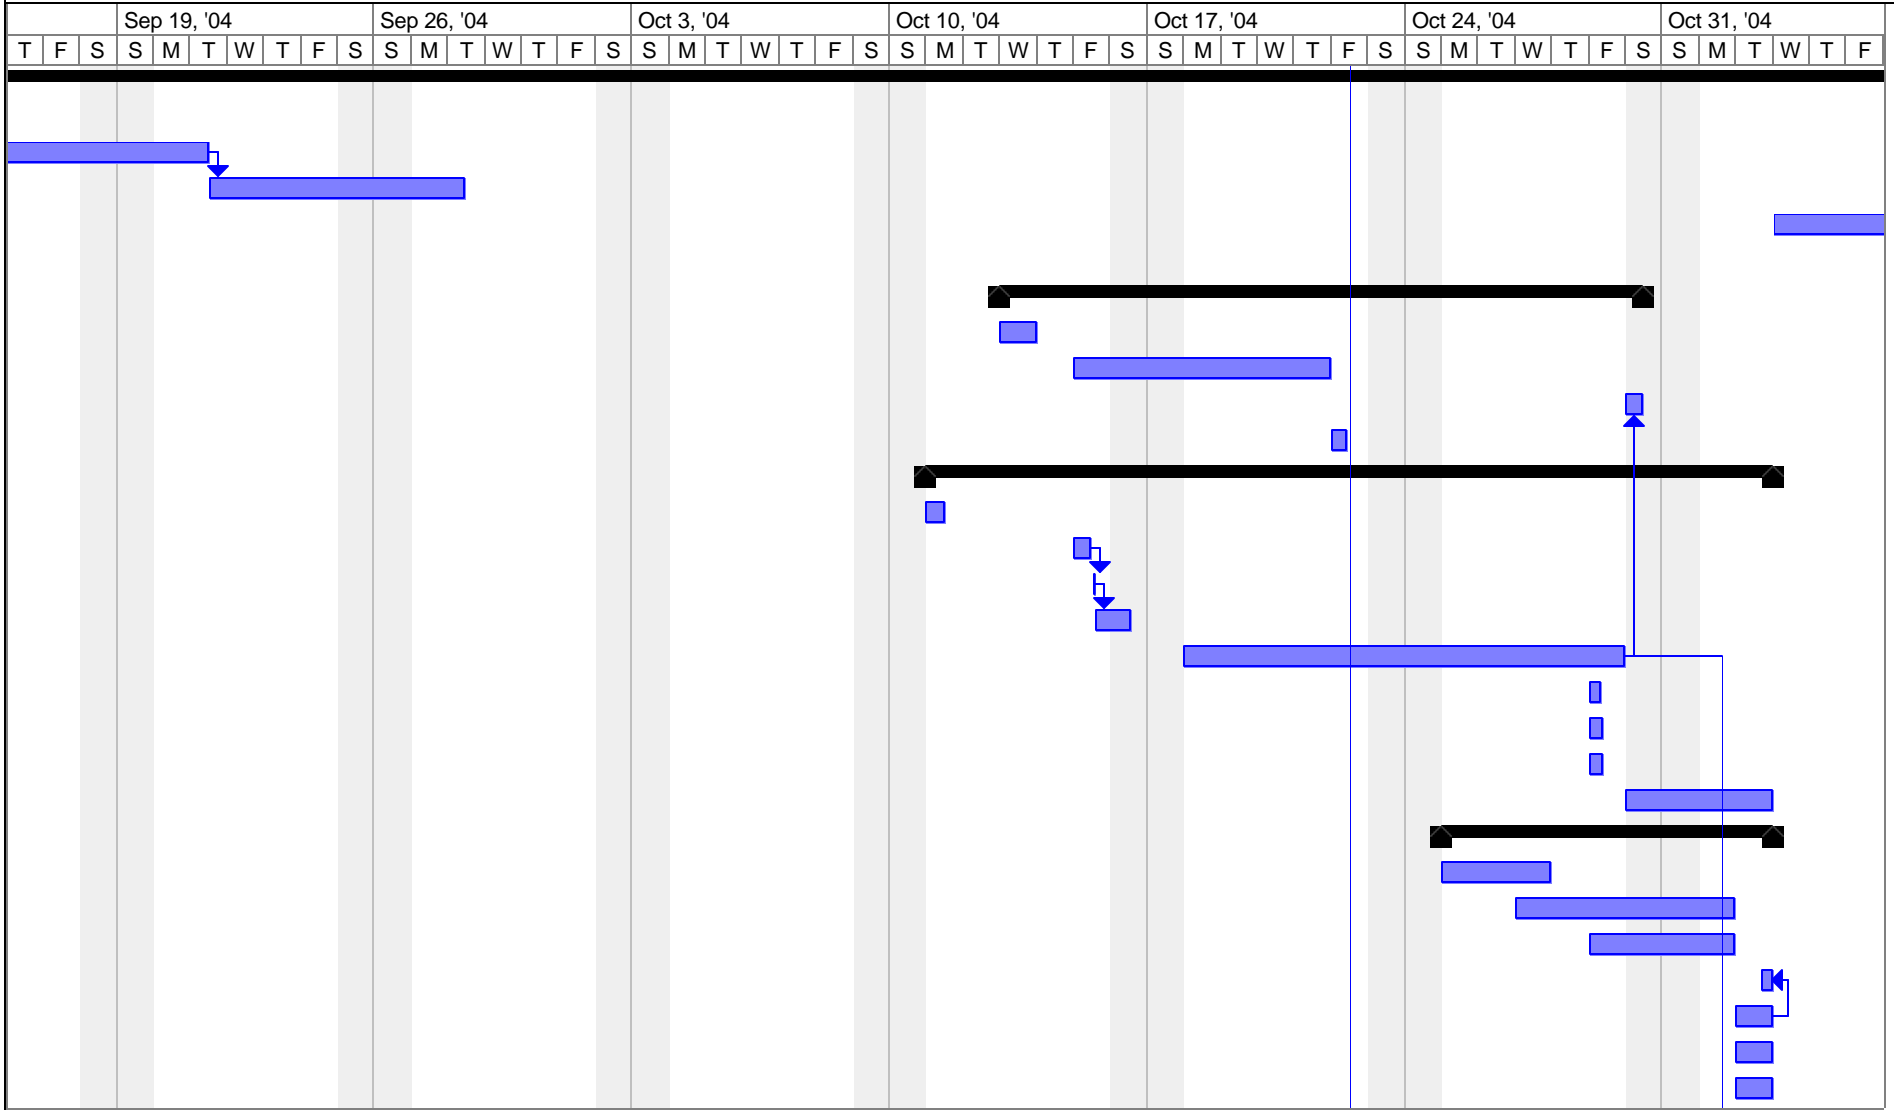

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

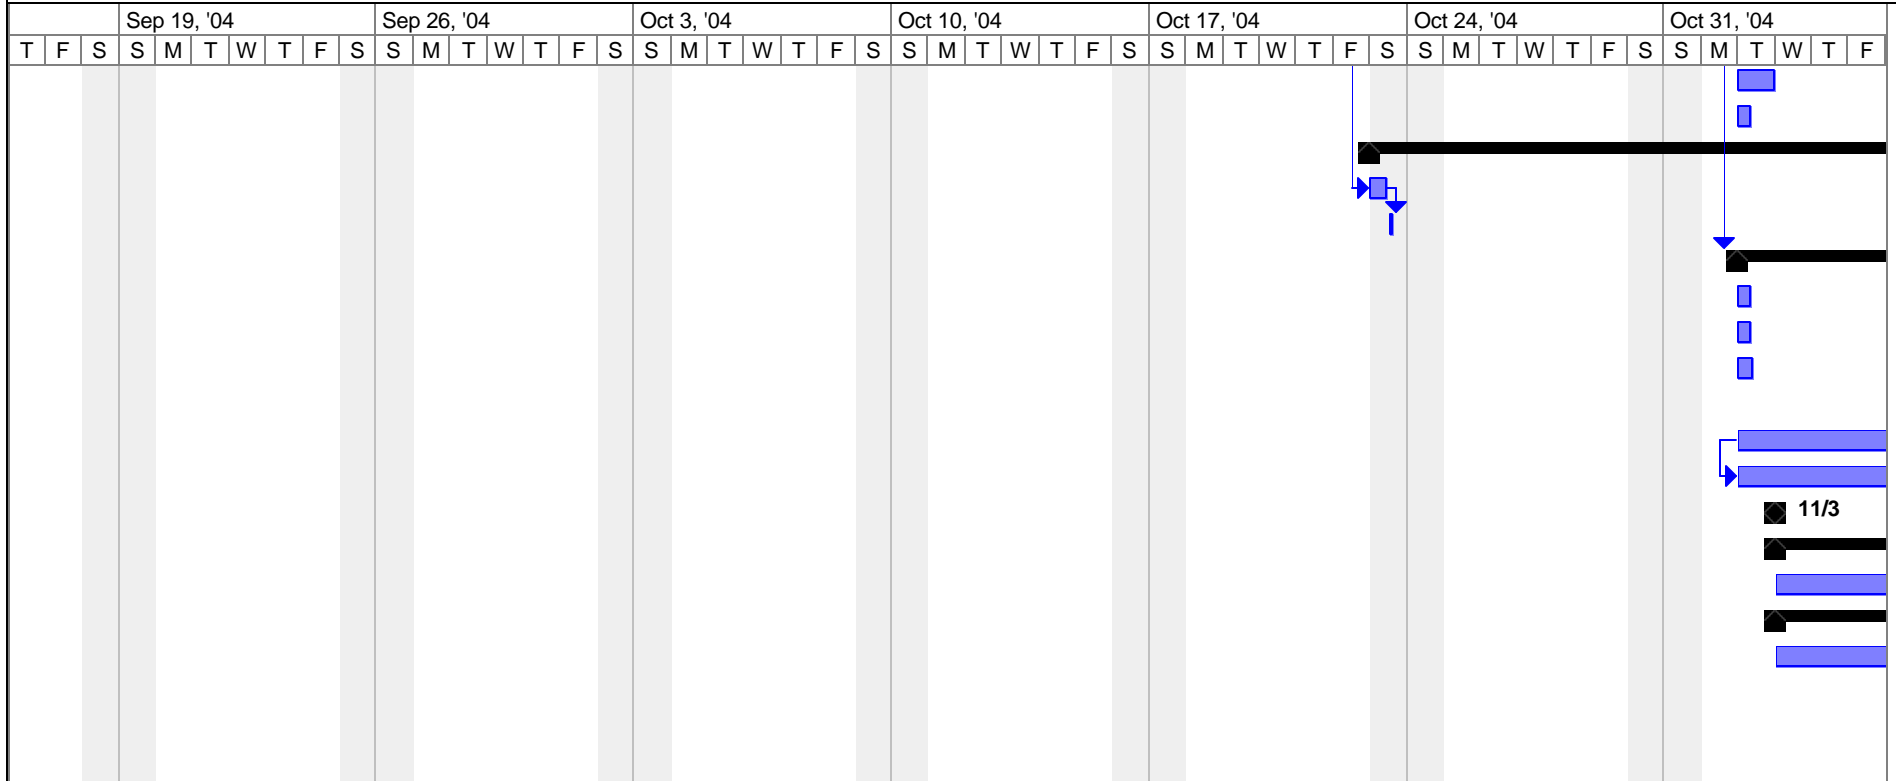


Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

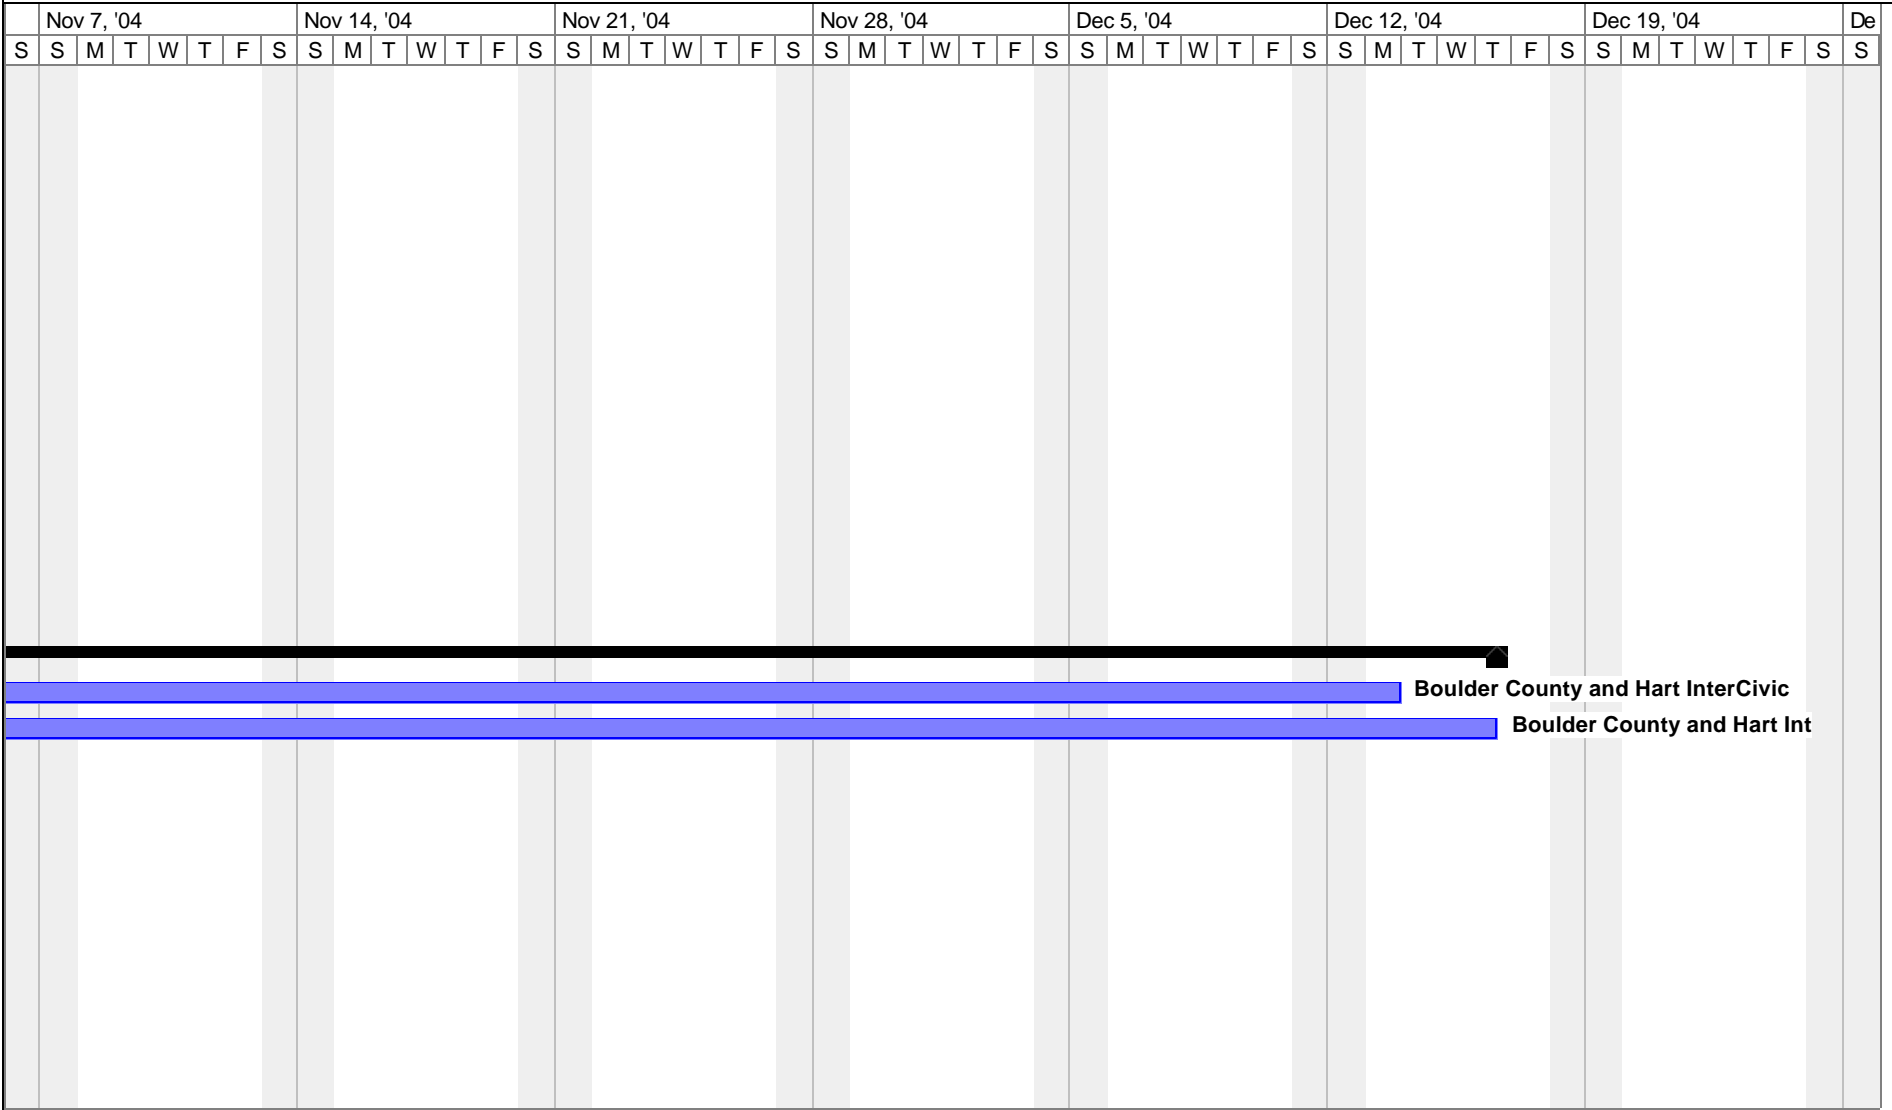










Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Nov 7, '04							Nov 14, '04							Nov 21, '04							Nov 28, '04							Dec 5, '04							Dec 12, '04							Dec 19, '04							De																
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S														










Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation










Nov 7, '04							Nov 14, '04							Nov 21, '04							Nov 28, '04							Dec 5, '04							Dec 12, '04							Dec 19, '04							De																
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S														

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation










Nov 7, '04							Nov 14, '04							Nov 21, '04							Nov 28, '04							Dec 5, '04							Dec 12, '04							Dec 19, '04							De																
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S														

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

Nov 7, '04							Nov 14, '04							Nov 21, '04							Nov 28, '04							Dec 5, '04							Dec 12, '04							Dec 19, '04							De																								
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S																						

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

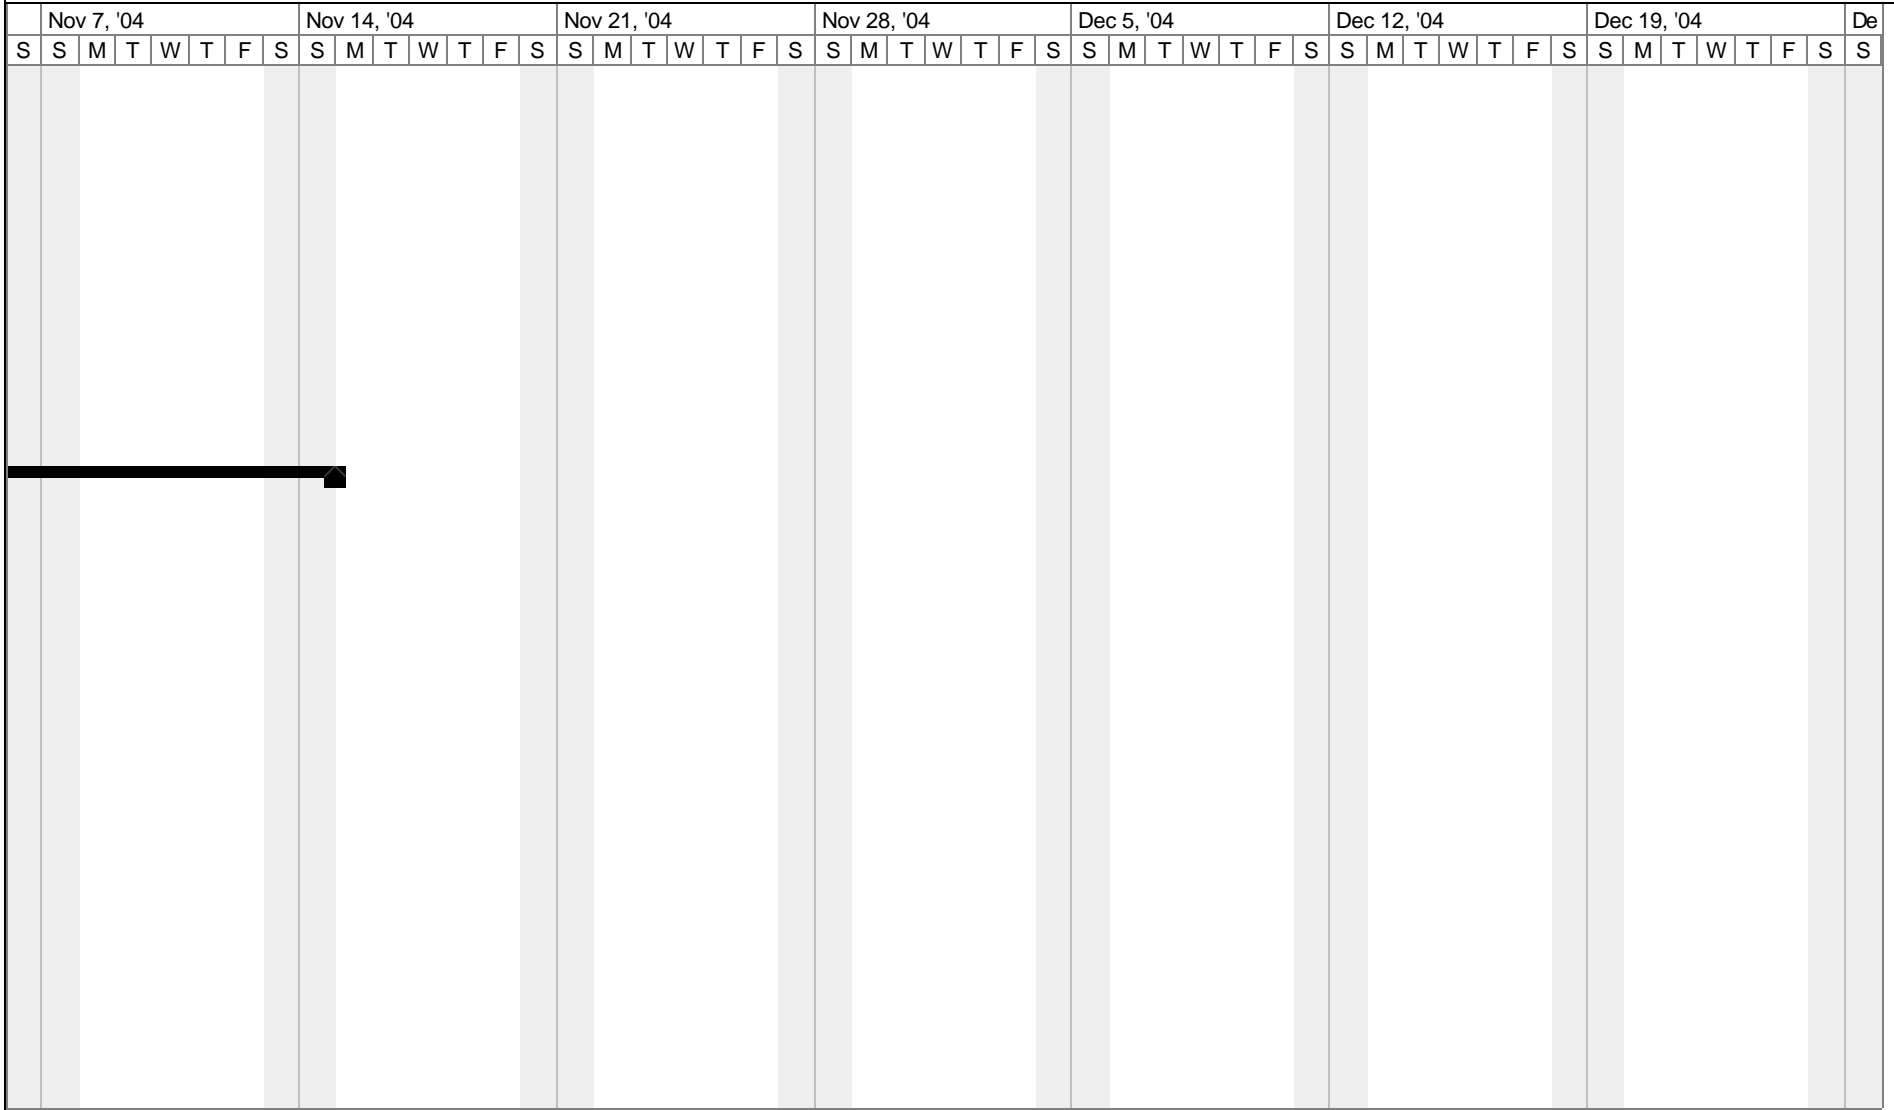





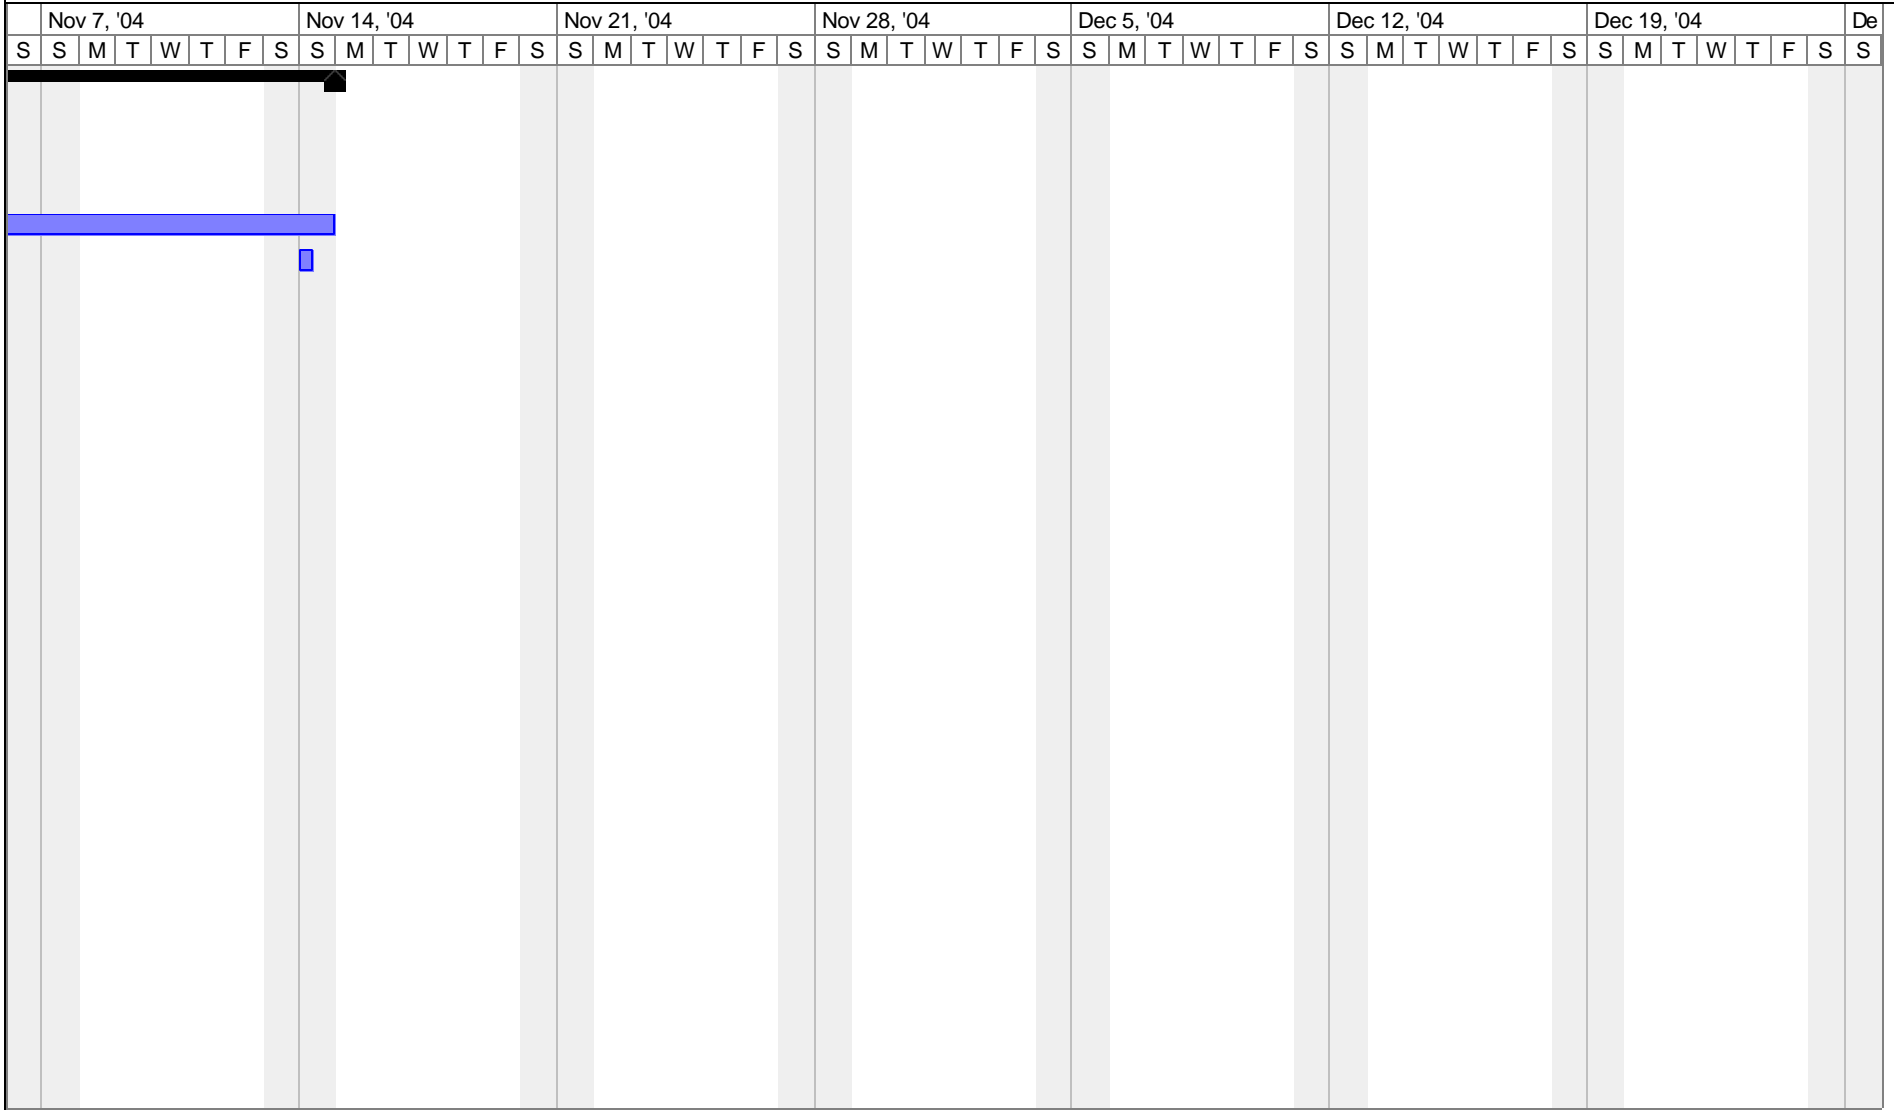

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation



Project: Boulder County Project Plan-F  
Date: Mon 4/12/04










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	














Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
<p>roj Teams erCivic Proj Teams</p>																																											

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation










26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation










26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation










26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T










Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T



Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation









26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Boulder County Project Plan-F  
Date: Mon 4/12/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Preliminary Project Plan  
Boulder County, Colorado  
Ballot Now System Implementation

26, '04					Jan 2, '05					Jan 9, '05					Jan 16, '05					Jan 23, '05					Jan 30, '05					Feb 6, '05					Feb 13, '05								
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Boulder County Project Plan-F Date: Mon 4/12/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
